

DURHAM • CHAPEL HILL • CARRBORO

**DCHC**

METROPOLITAN PLANNING ORGANIZATION

PLANNING TOMORROW'S TRANSPORTATION

# Status Report on Locally Administered Projects (LAP)

Dale McKeel, DCHC MPO Transportation Planner

[Dale.McKeel@durhamnc.gov](mailto:Dale.McKeel@durhamnc.gov)

# What are Locally Administered Projects (LAP)?

---

- LAP projects are administered by DCHC MPO member jurisdictions
- Jurisdictions are responsible for carrying out the design and construction of projects, or implementing funded programs
- LAP projects in DCHC MPO are almost exclusively bicycle, pedestrian, and transit
- LAP projects are funded using federal funding sources and typically have a 20 percent minimum non-federal match; since 2013 state funds cannot be used to match bike/ped projects so the match typically comes from local funds
- LAP projects are subject to the same state and federal requirements as federally funded projects managed by NCDOT
- NCDOT staff advise, approve, and oversee the expenditure of LAP project funds

## Overview of Report

---

- In November 2021 the DCHC MPO Board adopted the MPO's Federal Funding Policy
- Policy states that recipients will provide a brief report on the status of their locally administered projects (LAP) twice a year
- In addition to LAP projects funded through the MPO's Regional Flexible Funding (RFF), this report includes LAP projects funded through the STI / SPOT process
- Please provide feedback on how this report can be modified to be most useful

# Typical Project Delivery Steps

---

## Project Setup Phase

*Program Project in STIP and TIP*

*Identify Sources of Local Match*

*Execute Municipal Agreement between NCDOT and Local Government Agency*

## Preliminary Engineering Authorization (i.e., Engineering Phase)

*Procure Professional Services (Consultant)*

*Prepare Environmental Document*

*Prepare Design Plans*

## Right of Way Authorization (i.e., Right-of-Way Phase)

*Right of Way Acquisition*

*Utility Relocation*

*Receive Right of Way Certification from NCDOT*

*Prepare Contract Proposal and Estimate (PS&E)*

## Construction Authorization (i.e., Construction Phase)

*Advertise and Let Construction Contract*

*Construction & Administration*

*Final Inspection*

*Final Reimbursement*

## Project Closeout

# Federal Funding Sources

---

- CMAQ – Congestion Mitigation and Air Quality
- RAISE - Rebuilding American Infrastructure with Sustainability and Equity
- SRTS – Safe Routes to Schools
- STBGDA – Surface Transportation Block Grant – Direct Allocation
- TAP – Transportation Alternatives Program
- TAPDA - Transportation Alternatives Program – Direct Allocation




# GoTriangle Locally Administered Projects

---

# STIP ID #TL-0018 - 15-501/Eastowne Transit Access Improvements


|                                                  |                                                                                                         |
|--------------------------------------------------|---------------------------------------------------------------------------------------------------------|
| <b>Description</b>                               | Construct bus stop improvements, including bus bays, sidewalk connections at US 15-501 and Eastowne Dr. |
| <b>Project Manager</b>                           | Jay Heikes, GoTriangle                                                                                  |
| <b>Funding</b>                                   | Federal \$ 400,000<br>Orange Transit Plan \$ 100,000                                                    |
| <b>Status</b>                                    | Project Setup                                                                                           |
| <b>Estimated Completion Date / Add'l Details</b> | <del>2023</del> 2024                                                                                    |

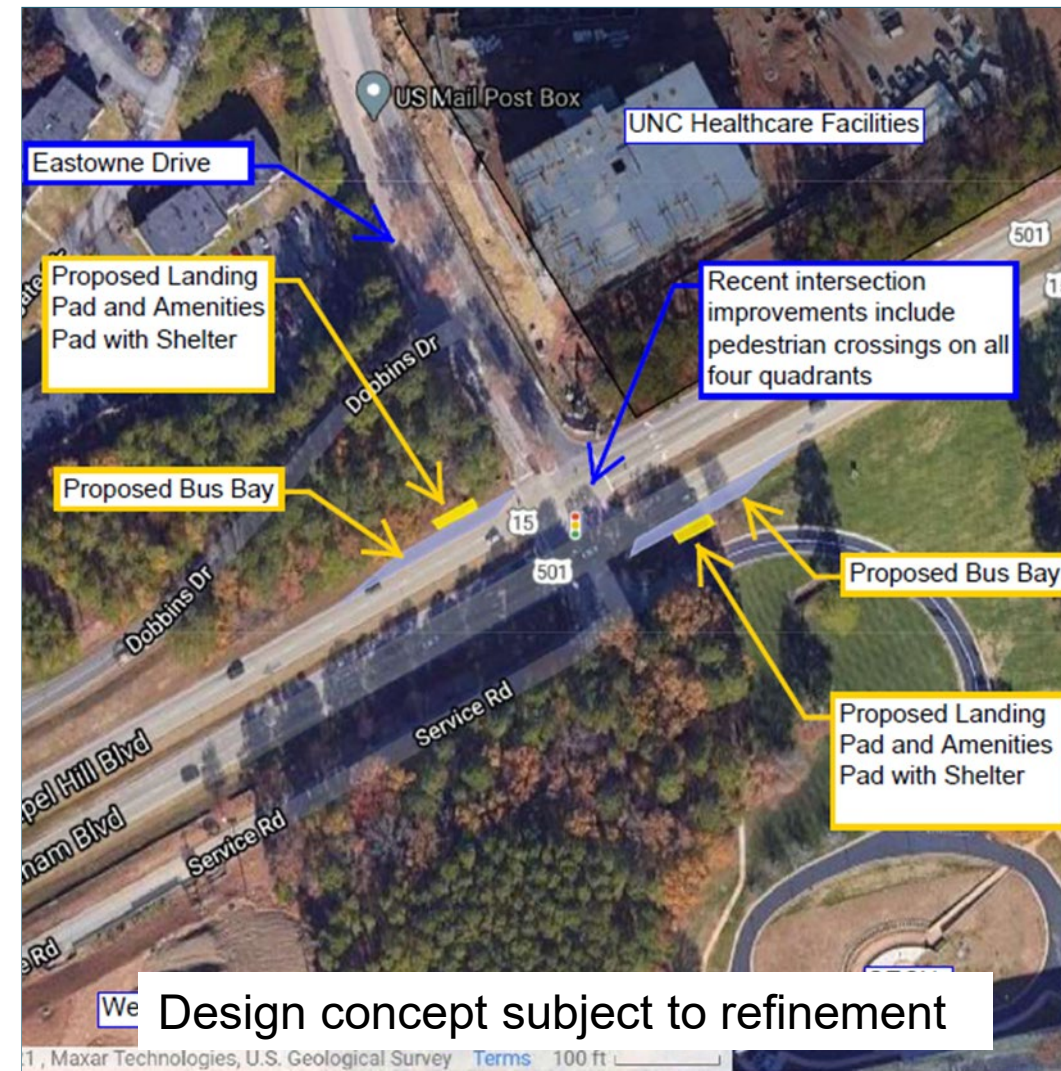



# STIP ID #TL-0025 – NC 54 / Falconbridge Transit Access Improvements

|                                           |                                                                                                                                                  |
|-------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------|
| Description                               | Construct bus stop improvements, including bus bays, sidewalk connections, crosswalk improvements NC 54 at Falconbridge Rd. and Huntingridge Dr. |
| Project Manager                           | Jay Heikes, GoTriangle                                                                                                                           |
| Funding                                   | Federal \$ 930,320<br>Durham Transit Plan \$ 232,580<br>(RFF Funding for Construction phase only)                                                |
| Status                                    | Engineering                                                                                                                                      |
| Estimated Completion Date / Add'l Details | <div>Spring 2024 2024</div> <div>Coordinate with NCDOT High Impact, Low Cost Project #48973</div>                                                |

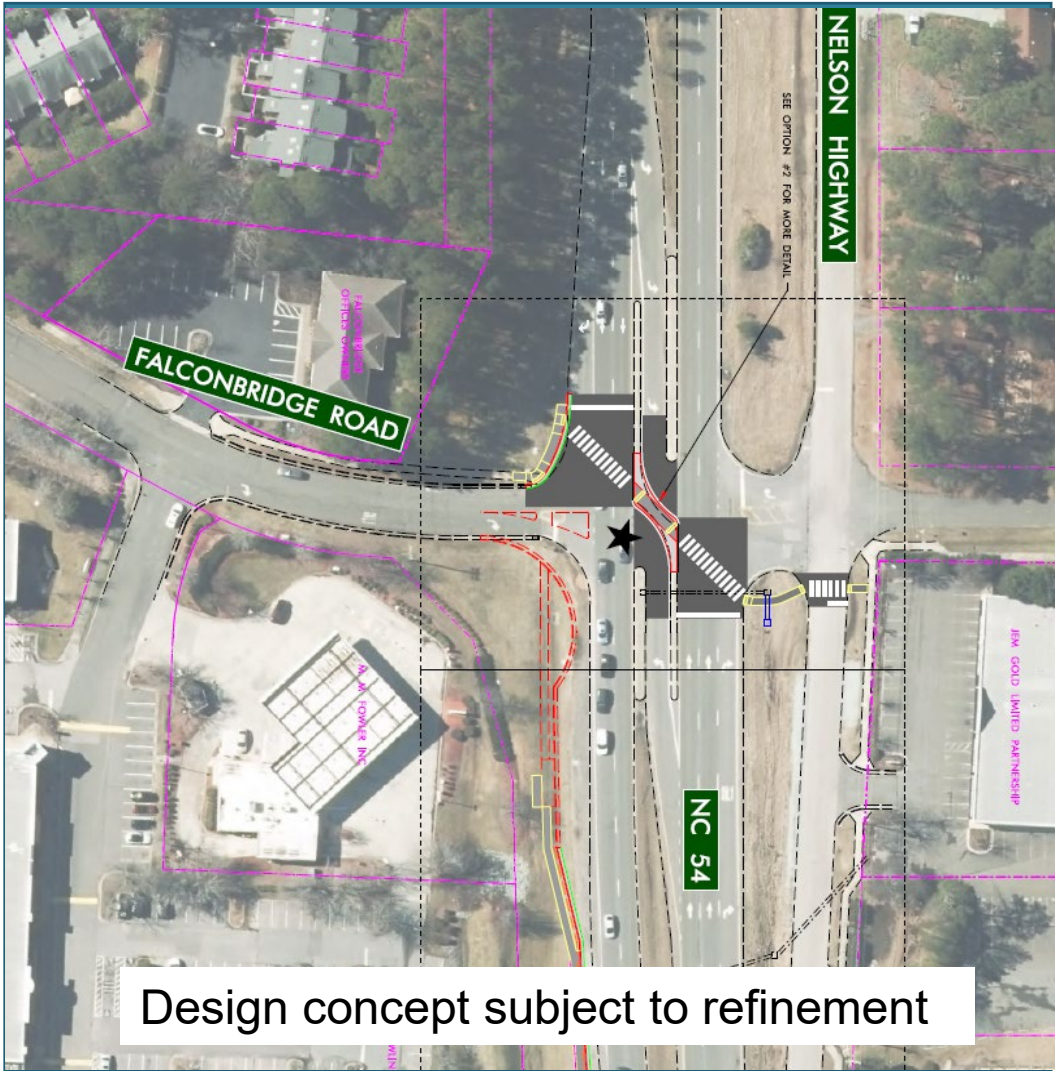



# Town of Carrboro Locally Administered Projects

---



# C-5181 Jones Creek Greenway

|                                  |                                                                                                                                                                                                                                                                             |
|----------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Description</b>               | Part of the upper Bolin Creek Greenway system, an approximately 800-foot paved multi-use path and pedestrian bridge connecting Lake Hogan Farm Road, in Lake Hogan Farms, with Orange County's Twin Creeks Greenway and the Morris Grove Elementary School on Eubanks Road. |
| <b>Project Manager</b>           | Tina Moon, Planning Department – Design<br>Ben Schmadeke, Public Works – Construction                                                                                                                                                                                       |
| <b>Funding</b>                   | Federal \$ 680,200 (CMAQ)<br>\$ 204,800 (STBGDA)                                                                                                                                                                                                                            |
| <b>Status</b>                    | Engineering. Plans are at 90% design                                                                                                                                                                                                                                        |
| <b>Estimated Completion Date</b> | Anticipate construction in FFY23                                                                                                                                                                                                                                            |





# U-4726DF – Bicycle Detector Loops


|                                  |                                                                                                                                                                                                                        |
|----------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Description</b>               | Installation of bicycle detector loops at three intersections downtown and at West Poplar/NC 54 West. A fourth location will be included in East Main Street resurfacing project.                                      |
| <b>Project Manager</b>           | Tina Moon, Planning Department – Design<br>Ben Schmadeke, Public Works – Construction                                                                                                                                  |
| <b>Funding</b>                   | Federal \$ 30,000<br>\$ 96,000 (STBGDA)                                                                                                                                                                                |
| <b>Status</b>                    | Engineering. Project was advertised for construction in 2017 & 2019 with no bidders. Bid packet being updated to meet current NCDOT standards. Plans at 75% 90% design with <del>one</del> two rounds of NCDOT review. |
| <b>Estimated Completion Date</b> | Anticipate construction in FFY23                                                                                                                                                                                       |





# C-5650 – South Greensboro Street Sidewalk

|                                  |                                                                                                                                                                                                          |
|----------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Description</b>               | Sidewalk along the west side of S. Greensboro St. from the northern end of Old Pittsboro Rd. to the NC-54 eastbound off-ramp, and on to the Public Works driveway.                                       |
| <b>Project Manager</b>           | Tina Moon, Planning Department – Design<br>Ben Schmadeke, Public Works – Construction                                                                                                                    |
| <b>Funding</b>                   | Federal \$ 714,000 (STBGDA)<br>\$ 440,000 (CMAQ)<br>\$ 206,343 (CORONA VIRUS RELIEF)<br>\$ 380,800 (STBGDA)<br>\$ 560,000 (RFF)<br><b>AND \$ 486,579 (OC Transit)</b>                                    |
| <b>Status</b>                    | Engineering. Plans are at 65% design. NCDOT is reviewing The project engineer is preparing a scope of work to address additional work related to a waterline replacement identified during NCDOT review. |
| <b>Estimated Completion Date</b> | Construction anticipated for FFY24                                                                                                                                                                       |

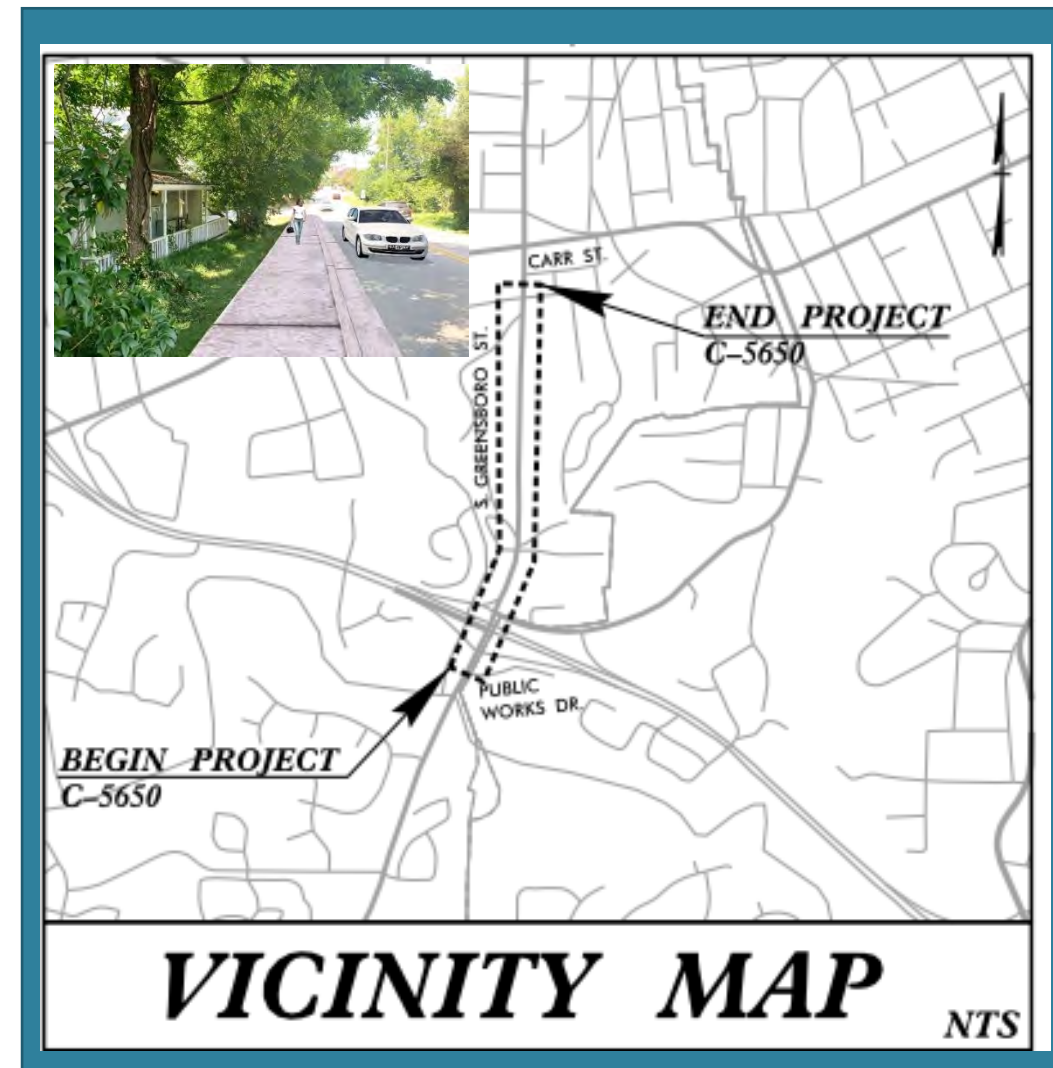


# EL-4828A – Morgan Creek Greenway

|                                  |                                                                                                                                                                                                                                                                                                                                                                   |
|----------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Description</b>               | <p>Paved greenway system that will ultimately connect Smith Level Road to University Lake with a potential spur to Carrboro High School.</p> <p>Phase 1 extends from SR 1919 (Smith Level Road) along the north side of Morgan Creek to a terminus point on the south side of Morgan Creek, for a total of approximately 1850 linear feet with two crossings.</p> |
| <b>Project Manager</b>           | Tina Moon, Planning Department – Design<br>Ben Schmadeke, Public Works – Construction                                                                                                                                                                                                                                                                             |
| <b>Funding</b>                   | <p>Federal \$ 730,000 (TAPDA)<br/>\$ 524,000 (STBGDA)<br/><b>AND \$ 374,836 (OC Transit for redesign &amp; CON)</b></p>                                                                                                                                                                                                                                           |
| <b>Status</b>                    | Engineering. Phase 1 was advertised in 2019, bids came in too high. After consulting with NCDOT, the Town is modifying the design prior to readvertising.                                                                                                                                                                                                         |
| <b>Estimated Completion Date</b> | <p><b>Redesign underway, plans at 30% close to 60% design. Flood study underway.</b></p> <p>Anticipate construction in FFY23.</p>                                                                                                                                                                                                                                 |





## BL-0044 - NC 54 Signalized Crossing in Carrboro

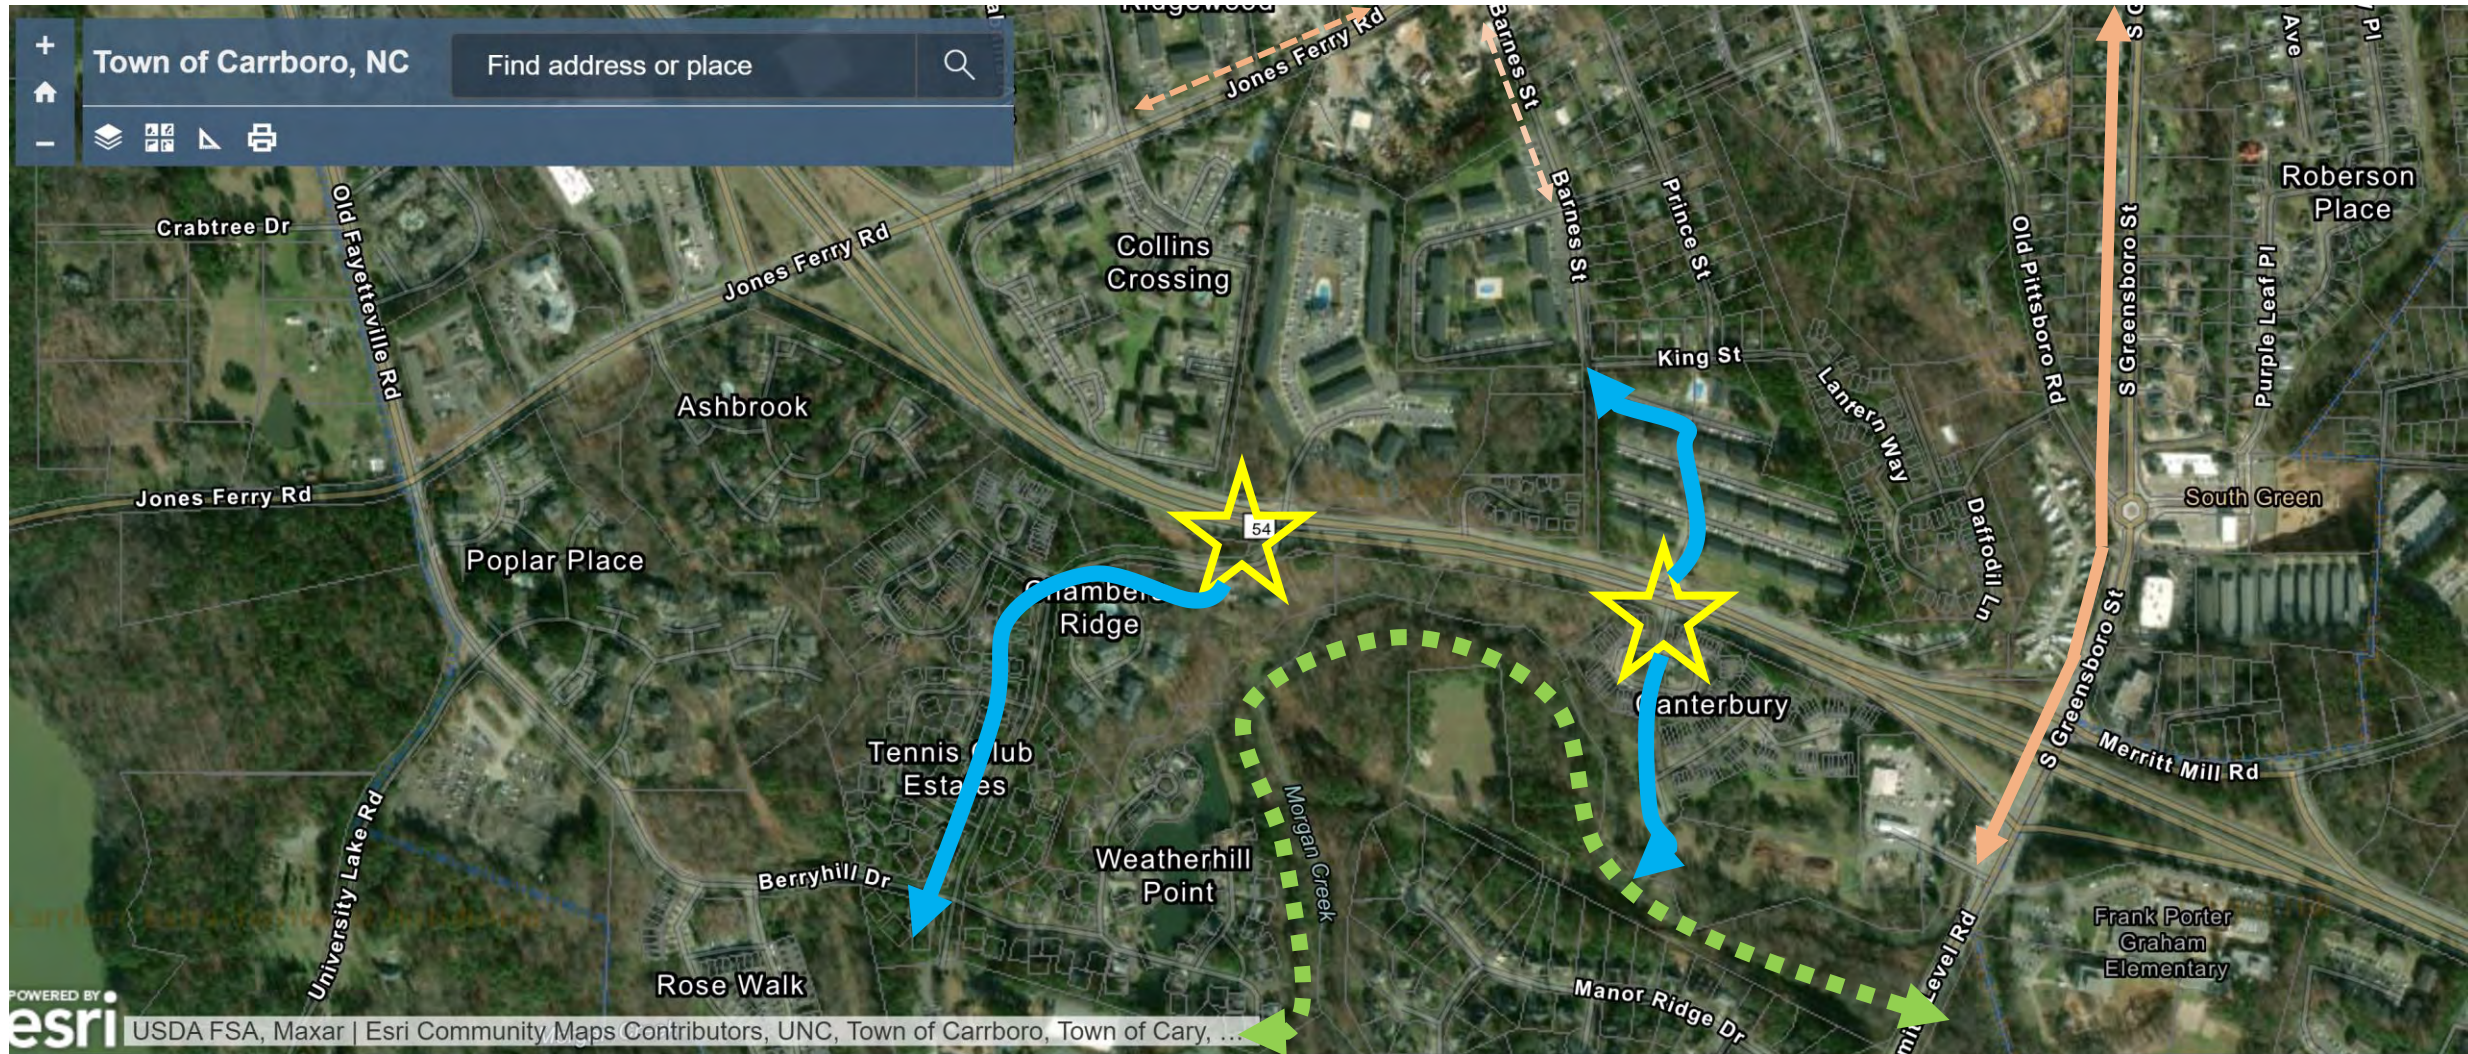



# Town of Chapel Hill Locally Administered Projects

---



# STIP ID C-5179 – Estes Drive Bike & Ped Improvements

|                                           |                                                                                                                                                                                                                        |
|-------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Description                               | On Estes Dr. between NC 86 and Caswell Dr., construct 5' bike lanes, a 5' sidewalk on the south side, and a 10' multiuse path on the north side. Crossing improvements at the MLK intersection and along the corridor. |
| Project Manager                           | Bergen Watterson                                                                                                                                                                                                       |
| Funding                                   | Federal \$5,051,757<br>(plus \$1,155,576 local match)                                                                                                                                                                  |
| Status                                    | Under construction                                                                                                                                                                                                     |
| Estimated Completion Date / Add'l Details | <del>Summer 2023</del> Fall 2023                                                                                                                                                                                       |





# STIP ID EB-5721 – Fordham Sidepath


|                                           |                                                                                                                              |
|-------------------------------------------|------------------------------------------------------------------------------------------------------------------------------|
| Description                               | Construct a sidepath along Fordham Blvd. between Cleland Dr. and Willow Dr. Add traffic calming measures at trail crossings. |
| Project Manager                           | Marcia Purvis/Bergen Watterson                                                                                               |
| Funding                                   | Federal \$1,256,000<br>(plus \$1,126,200 local match)                                                                        |
| Status                                    | Seeking construction authorization                                                                                           |
| Estimated Completion Date / Add'l Details | <del>Fall 2023, assuming construction contract award this fall</del> <i>Spring 2024</i>                                      |





# STIP ID EB-5886B – Estes Drive Ext. Bike & Ped Improvements

|                                                  |                                                                                                          |
|--------------------------------------------------|----------------------------------------------------------------------------------------------------------|
| <b>Description</b>                               | Construct bike and pedestrian improvements along Estes Drive Ext. between NC 86 and the Carrboro border. |
| <b>Project Manager</b>                           | Bergen Watterson                                                                                         |
| <b>Funding</b>                                   | Federal \$3,174,000<br>(plus \$901,000 local match)                                                      |
| <b>Status</b>                                    | Project Setup                                                                                            |
| <b>Estimated Completion Date / Add'l Details</b> | Project initiation anticipated <del>fall 2022</del> <i>spring 2023</i>                                   |

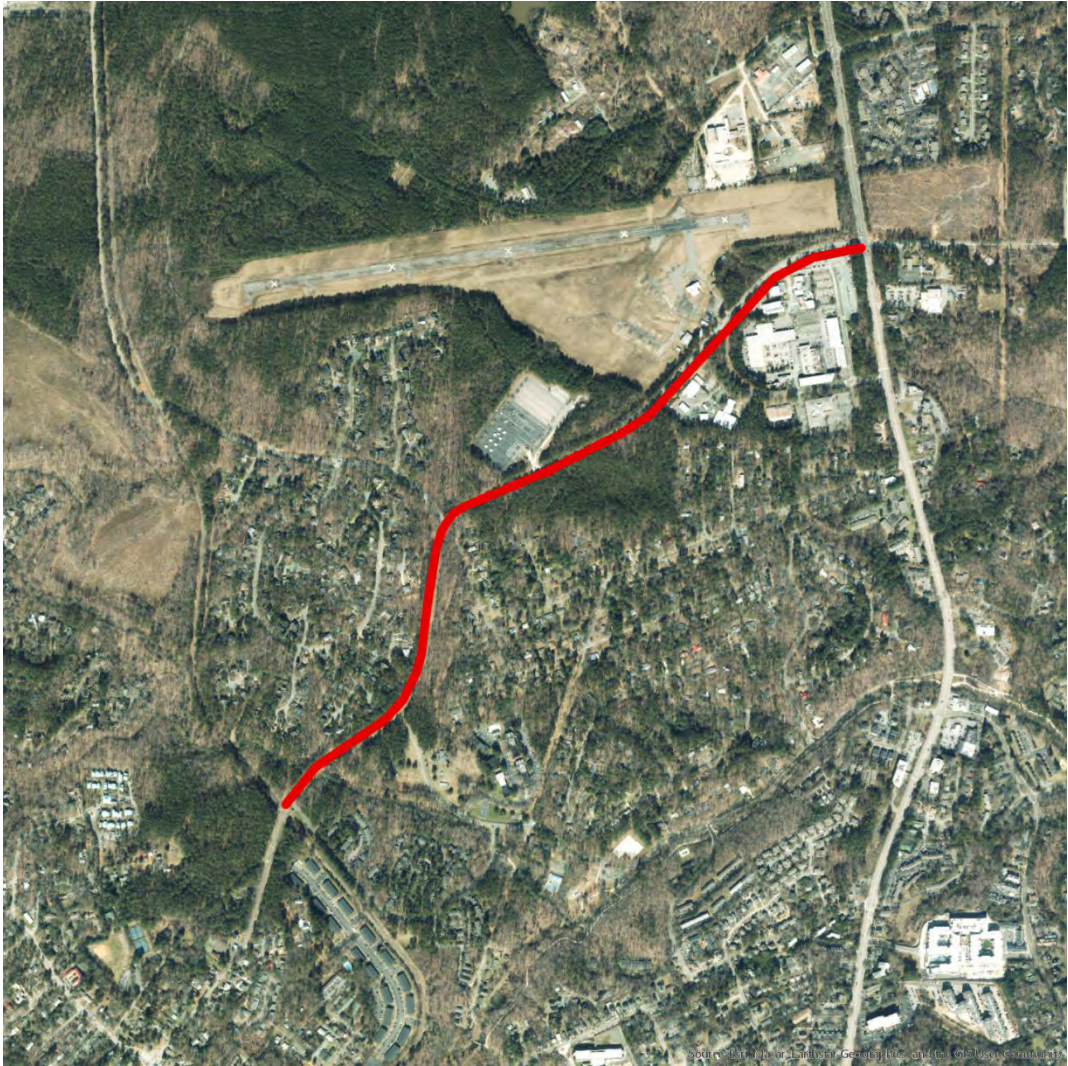



# STIP ID EB-5998 – Fordham Sidepath Extension

|                                           |                                                                                                  |
|-------------------------------------------|--------------------------------------------------------------------------------------------------|
| Description                               | Construct multiuse paths along both sides of Fordham Blvd. between Willow Dr. and Old Durham Rd. |
| Project Manager                           | Bergen Watterson                                                                                 |
| Funding                                   | Federal \$1,798,000<br>(plus \$450,000 local match)                                              |
| Status                                    | Project Setup                                                                                    |
| Estimated Completion Date / Add'l Details | Project initiation anticipated <del>summer 2023</del><br>fall 2023                               |





# STIP ID U-4726IK – Homestead Road Bike & Ped Improvements

|                                                  |                                                                                                                                                                                     |
|--------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Description</b>                               | Construct a sidewalk, multiuse path, and bike lanes along Homestead Rd. in Chapel Hill between Weaver Dairy Ext. and Seawell School Rd. Sidewalk on east side of Seawell School Rd. |
| <b>Project Manager</b>                           | Chris Roberts                                                                                                                                                                       |
| <b>Funding</b>                                   | Federal \$1,040,000<br>(plus \$487,994 local match)                                                                                                                                 |
| <b>Status</b>                                    | Construction Authorization                                                                                                                                                          |
| <b>Estimated Completion Date / Add'l Details</b> | Bid anticipated <del>summer/fall 2022</del> <i>spring 2023</i>                                                                                                                      |





# STIP ID BL-0044 – NC 54 Pedestrian Improvements

|                                                  |                                                                                                                                                                         |
|--------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Description</b>                               | Construct sidewalk and install pedestrian signals and crosswalks on NC 54 from Westbrook Drive in Carrboro to west of the US 15-501 / NC 86 interchange in Chapel Hill. |
| <b>Project Manager</b>                           | NCDOT – Brian Thomas                                                                                                                                                    |
| <b>Funding</b>                                   | Federal \$978,000 (includes \$170,000 CH local discretionary)<br>(plus \$150,000 Carrboro local match plus \$400,000 State match)                                       |
| <b>Status</b>                                    | Design                                                                                                                                                                  |
| <b>Estimated Completion Date / Add'l Details</b> | NCDOT managing project with input from Chapel Hill and Carrboro                                                                                                         |






# City of Durham Locally Administered Projects

---




# City Of Durham LAP Projects

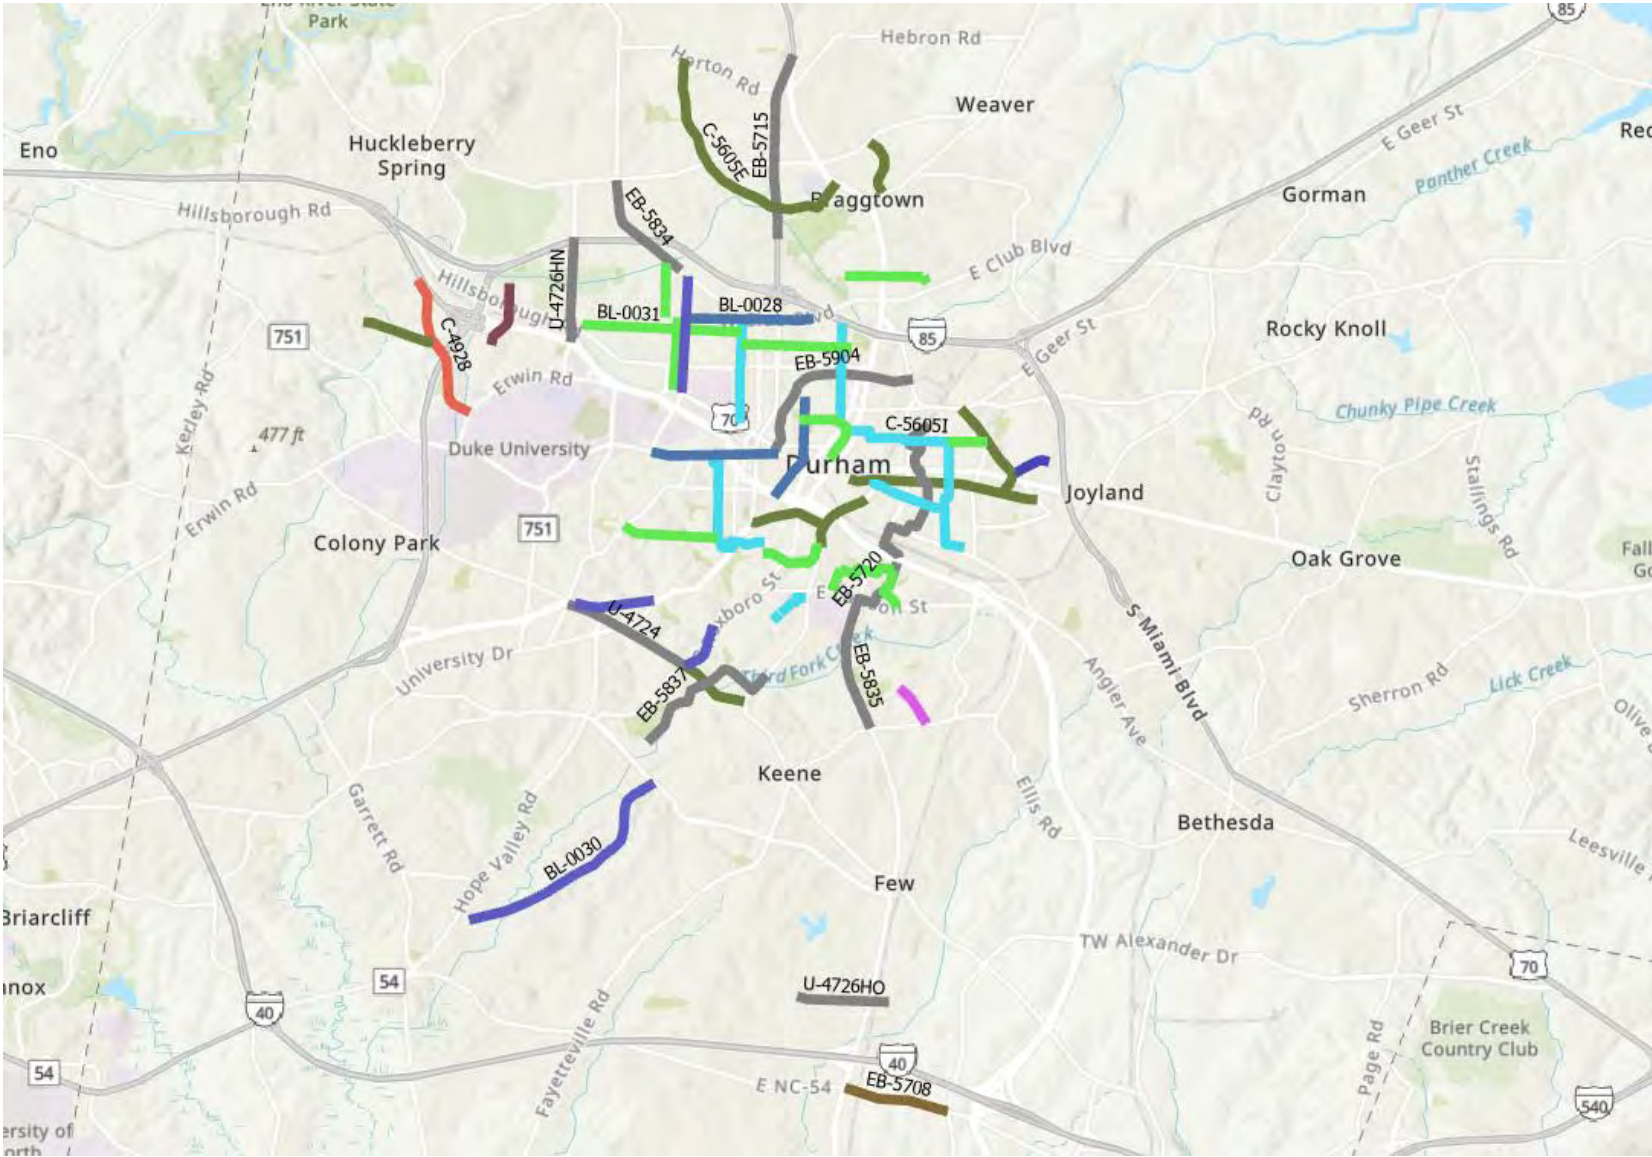






# City Of Durham LAP Projects Estimated Completion Dates

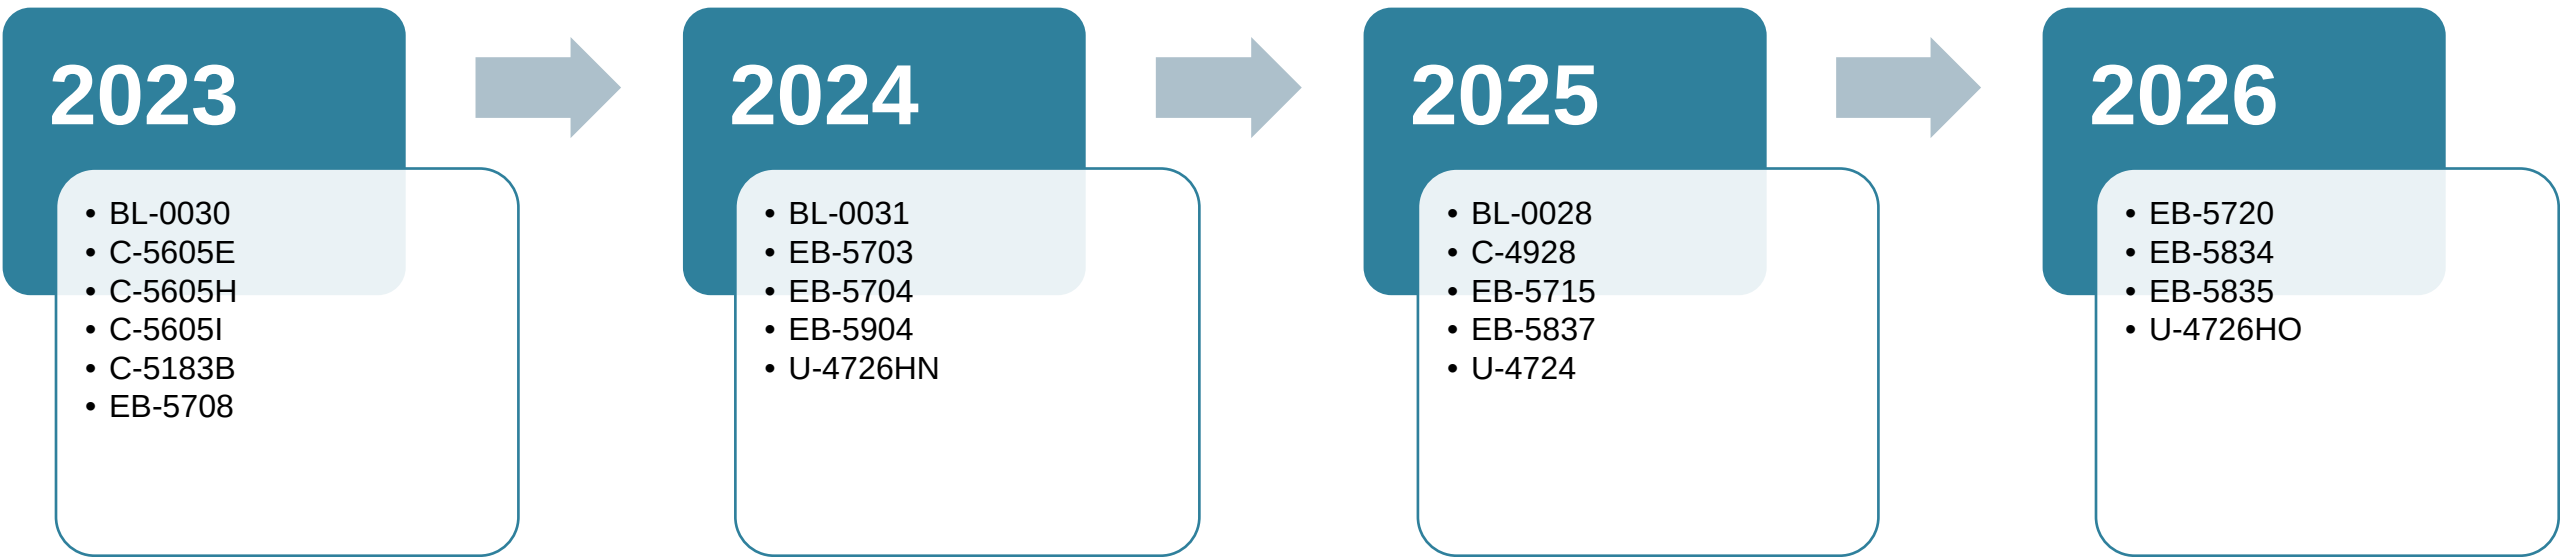



# Breakdown Of Project Types

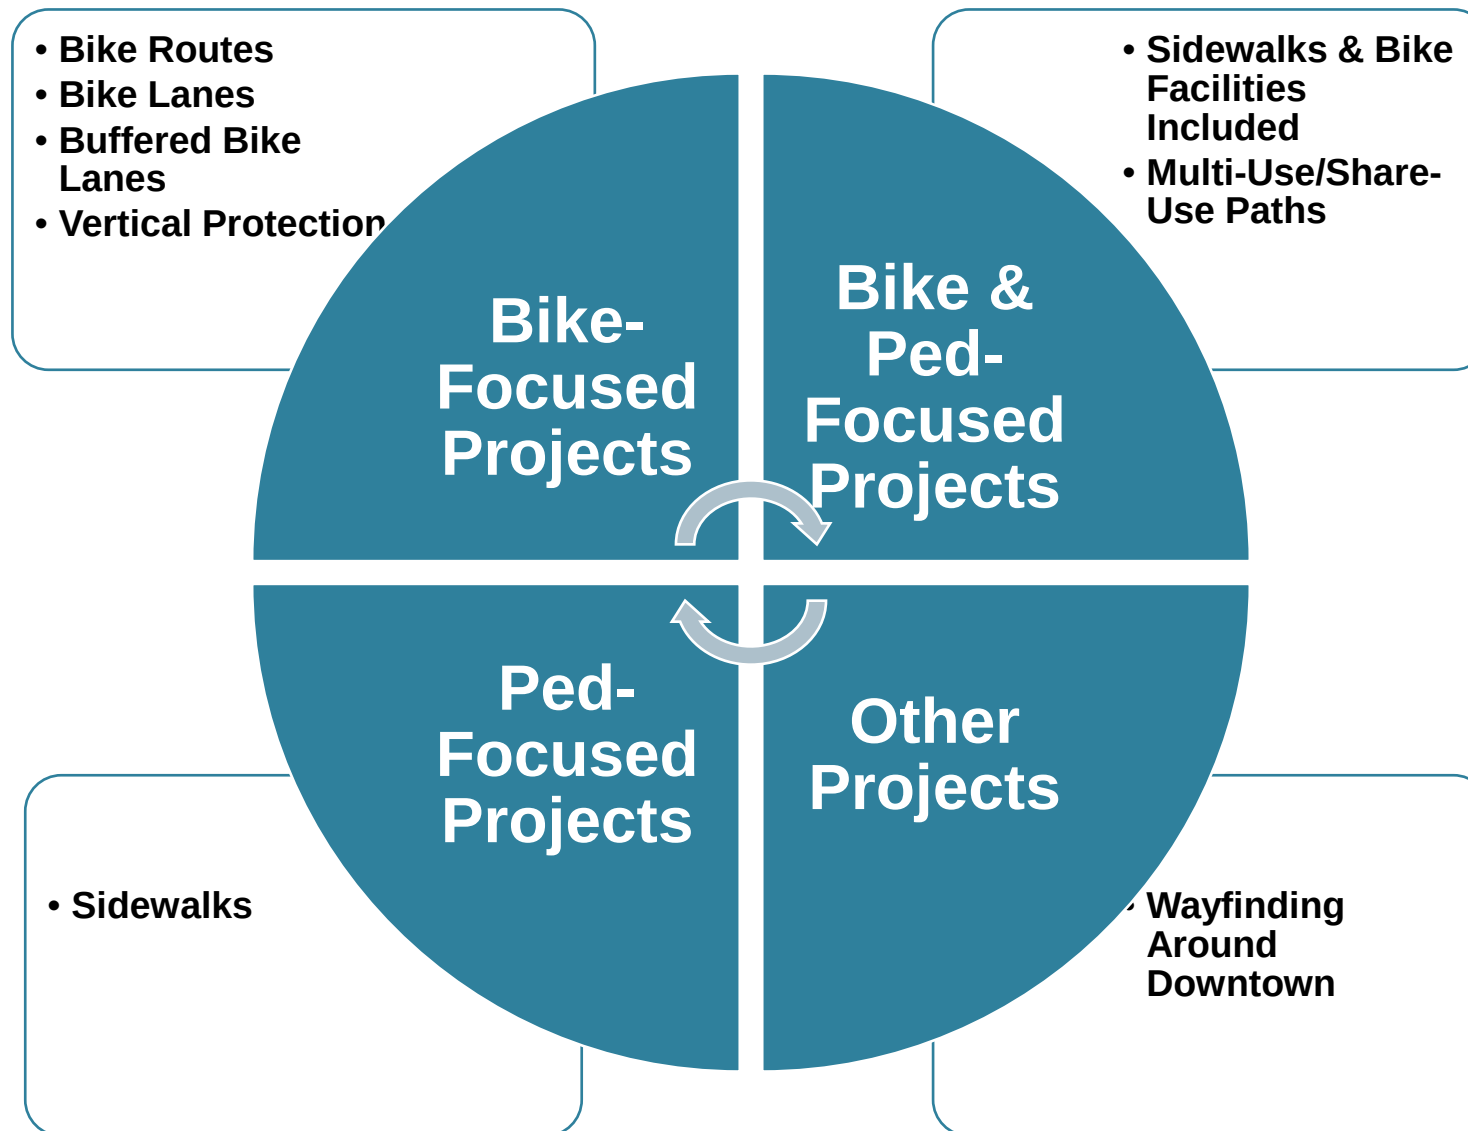








# BL-0031 – Durham Neighborhood Bike Routes II

|                                           |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |
|-------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Description                               | <p><b>Design and construct bicycle boulevards using signs, pavement markings, and speed and volume management measures to give priority to bicyclists.</b></p> <ul style="list-style-type: none"><li>• Englewood Ave (Georgia Ave to Watts St)</li><li>• Knox St (Watts St to Acadia)</li><li>• Bivins St (Chapel Hill Rd to Arnette Ave)</li><li>• Iredell St (Main St to West Club Blvd)</li><li>• Maryland Ave (West Club Blvd to Ellerbee Creek Trail)</li><li>• Cleveland St / Corporation St (Holloway St to Rigsbee Ave)</li><li>• Juniper St (Spruce St to Guthrie Ave)</li><li>• Lincoln St / Grant St (Lawson St to Lakeland St)</li><li>• Ridgeway Ave / Lakeland St (Lawson St to Mathison St)</li><li>• Lavender Ave (Elgin St to Stephenson St)</li><li>• Stephenson St (Lavender Ave to Club Blvd)</li><li>• Umstead St / Lodge St (Fayetteville St to Fargo St)</li></ul> |
| Project Manager                           | Erin Convery, Transportation                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |
| Funding                                   | Federal \$282,723 (STBGDA)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |
| Status                                    | Project Set Up                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            |
| Estimated Completion Date / Add'l Details | 2024                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |

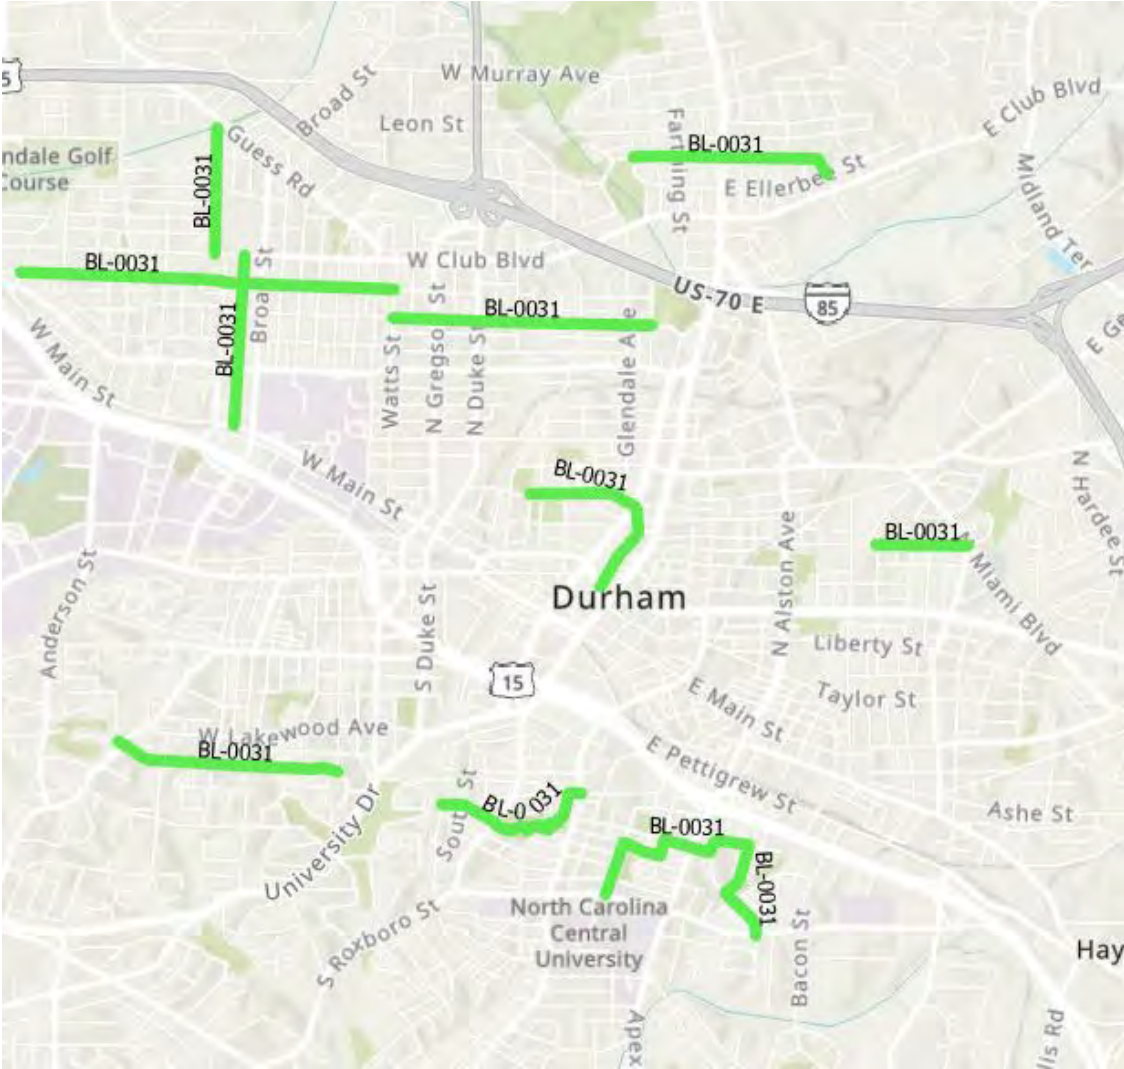






# C-5605E – Durham Bicycle Lane Striping


|                                           |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
|-------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Description                               | <div>Stripe eight miles of bicycle lanes in the City of Durham.</div> <div><div><div>•</div><div>Liberty St (Dillard to N Miami Blvd)</div></div><div><div>•</div><div>Fayetteville St (Main St to East Umstead)</div></div><div><div>•</div><div>Lakewood (Fayetteville St to Duke St)</div></div><div><div>•</div><div>N Miami Blvd (E Geer St to Raynor)</div></div><div><div>•</div><div>Stadium/Olympic (Roxboro to Horton)</div></div><div><div>•</div><div>Raynor (Liberty to Miami)</div></div><div><div>•</div><div>E Cornwallis Rd (S Roxboro St to Fayetteville St)</div></div><div><div>•</div><div>American Dr (Constitution to Morreene)</div></div><div><div>•</div><div>Meriwether Dr (E Carver to Old Oxford)</div></div></div> |
| Project Manager                           | <div><del>Todd Tingle</del>, Lisa Smith, General Services</div>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
| Funding                                   | Federal \$663,336 (CMAQ)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |
| Status                                    | Construction (Contracting)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       |
| Estimated Completion Date / Add'l Details | <div><del>11/1/2022</del> 8/1/2023</div>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |

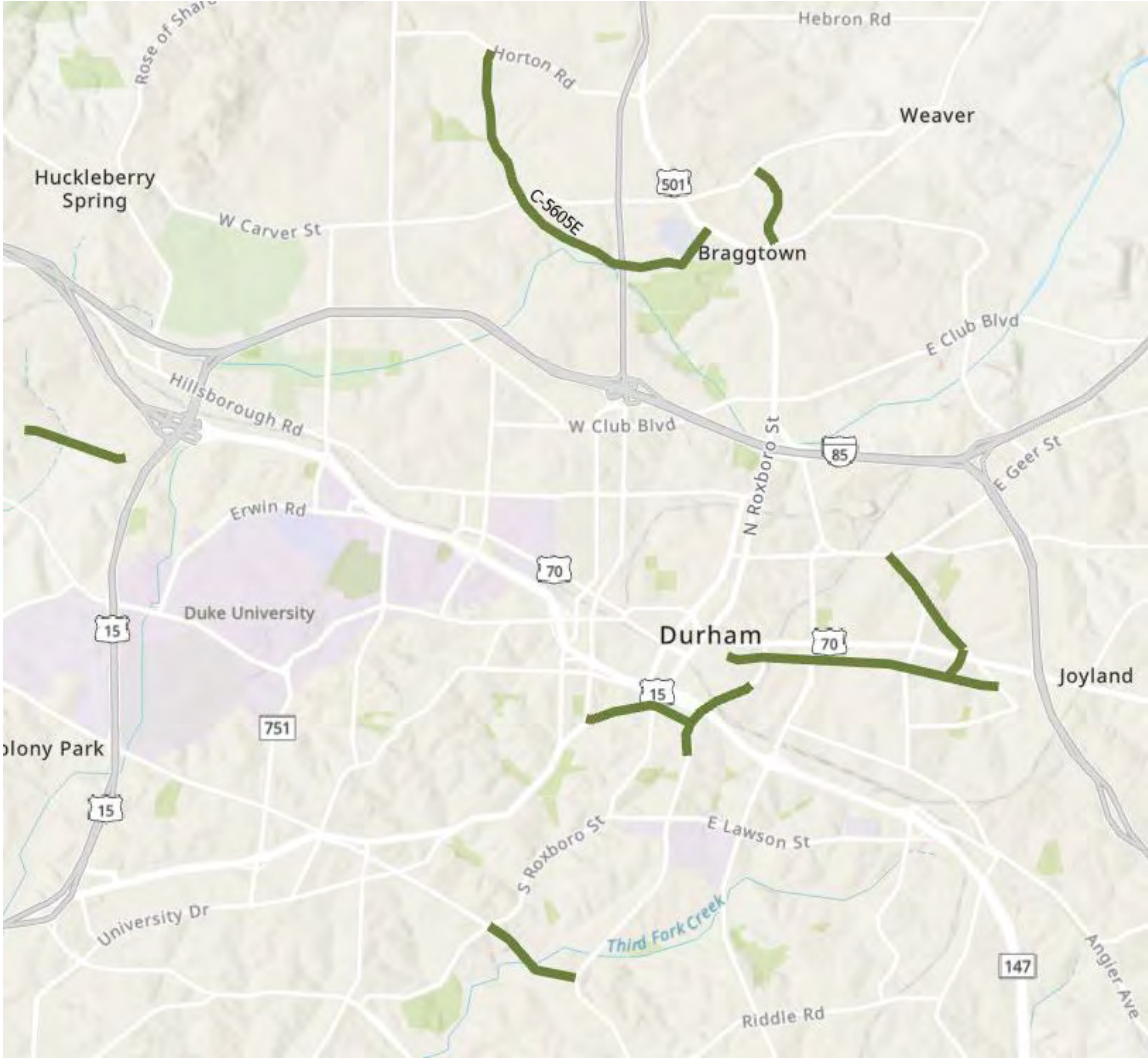



# BL-0028 – Durham Bike Facilities II

|                                           |                                                                                                                                                                                                                                                                                    |
|-------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Description                               | <b>Construct buffered bicycle lanes:</b> <ul style="list-style-type: none"><li>West Club Blvd (Washington St to Broad St)</li><li>Blackwell St / Corcoran St / Foster St corridor (ATT at Morehead St to Washington St)</li><li>Chapel Hill St (Ramseur St to Swift Ave)</li></ul> |
| Project Manager                           | Erin Convery, Transportation                                                                                                                                                                                                                                                       |
| Funding                                   | Federal \$851,000 (CMAQ, STBGDA)                                                                                                                                                                                                                                                   |
| Status                                    | Project Set Up                                                                                                                                                                                                                                                                     |
| Estimated Completion Date / Add'l Details | 2025                                                                                                                                                                                                                                                                               |

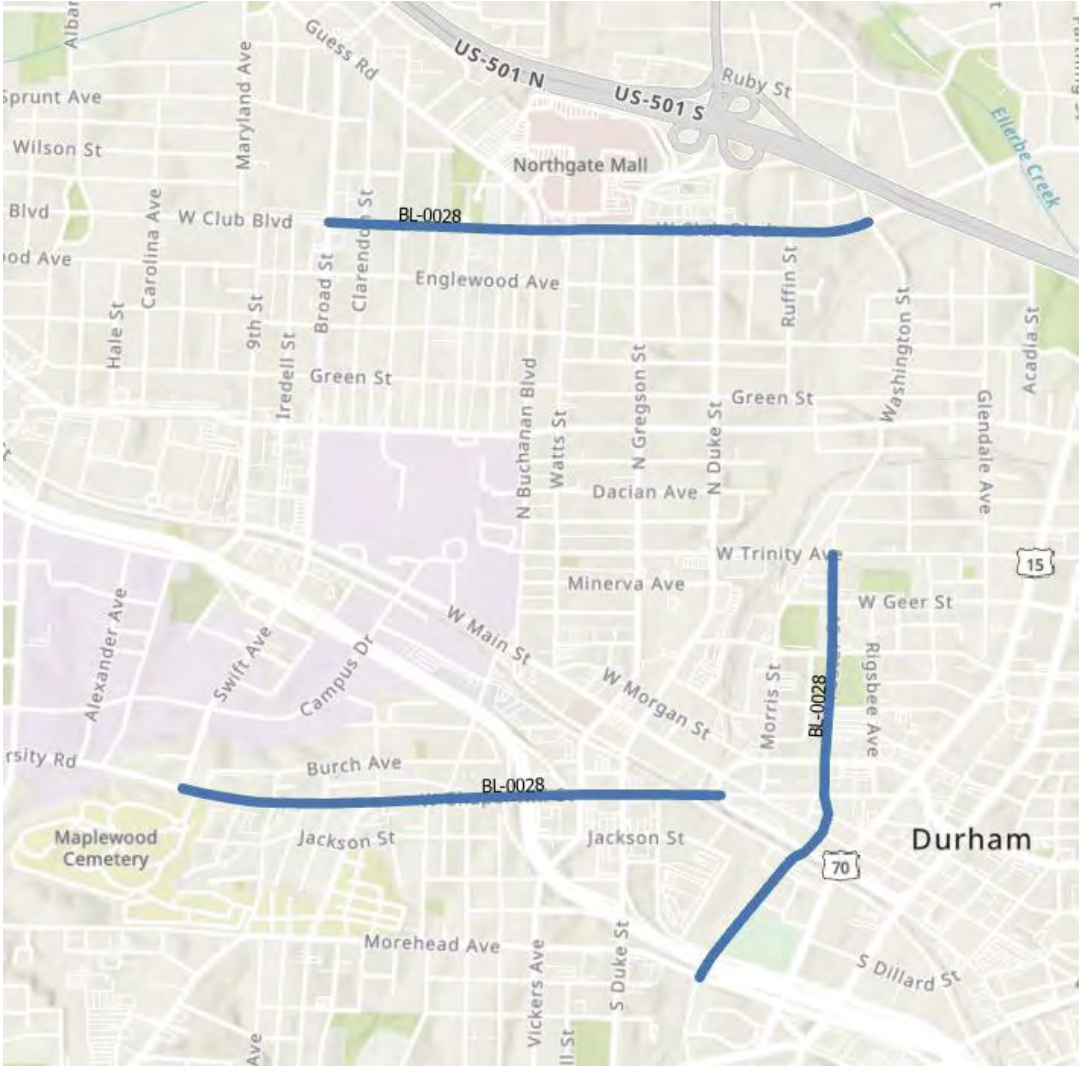






# BL-0030 – Vertical Protection


|                                           |                                                              |
|-------------------------------------------|--------------------------------------------------------------|
| Description                               | Add vertical protection to buffered bicycle lanes in Durham. |
| Project Manager                           | Erin Convery, Transportation                                 |
| Funding                                   | Federal \$172,035 (STBGDA)                                   |
| Status                                    | Project Set Up                                               |
| Estimated Completion Date / Add'l Details | 2023                                                         |

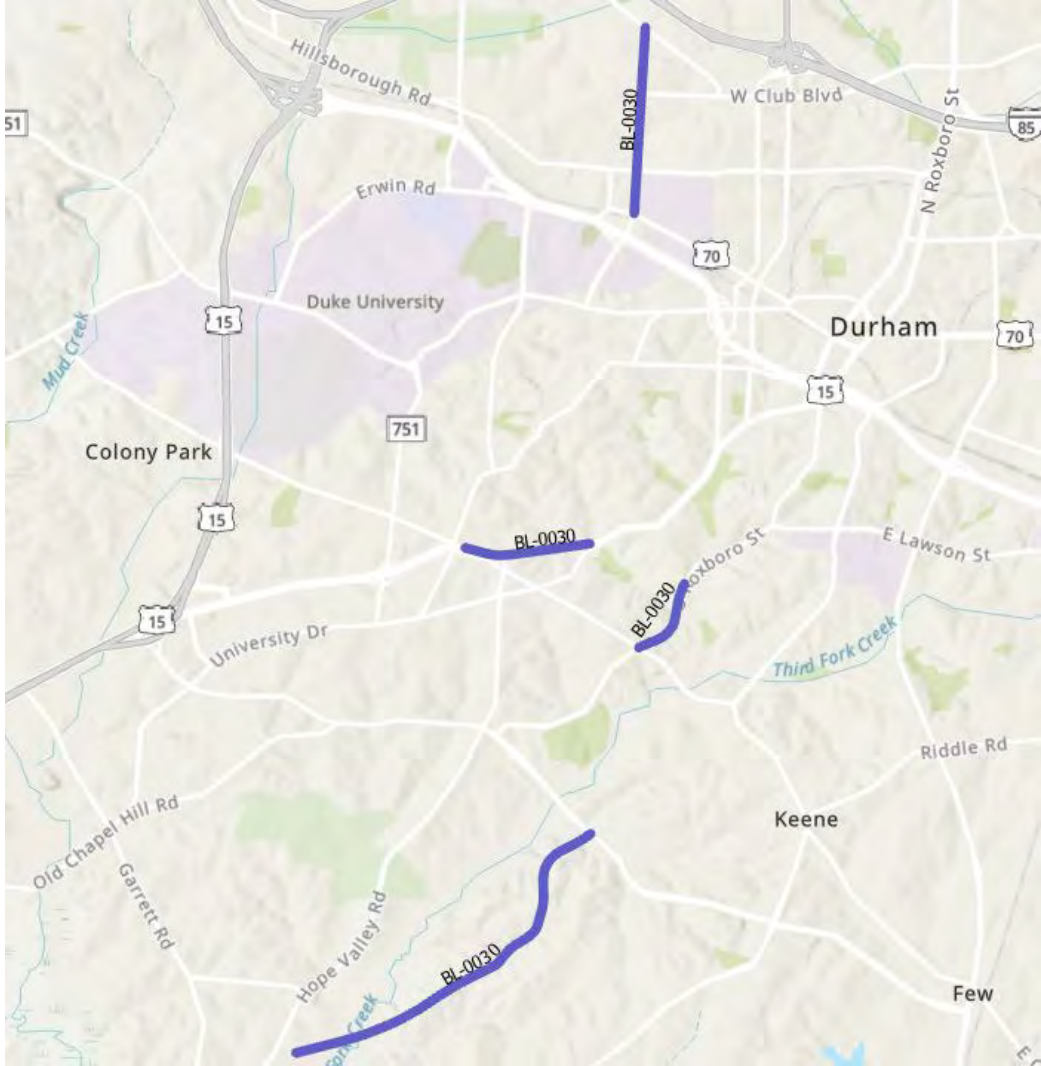



# C-4928 – Morreene Rd

|                                           |                                                                                                     |
|-------------------------------------------|-----------------------------------------------------------------------------------------------------|
| Description                               | Construct bike lanes and sidewalks along Morreene Rd in Durham, from Neal Rd to SR 1320 (Erwin Rd). |
| Project Manager                           | David Cates, Public Works                                                                           |
| Funding                                   | Federal <del>\$7,923,000</del> \$8,344,981 (CMAQ, STBGDA, STP-DA, BGANY)                            |
| Status                                    | Right Of Way                                                                                        |
| Estimated Completion Date / Add'l Details | 6/1/2025                                                                                            |

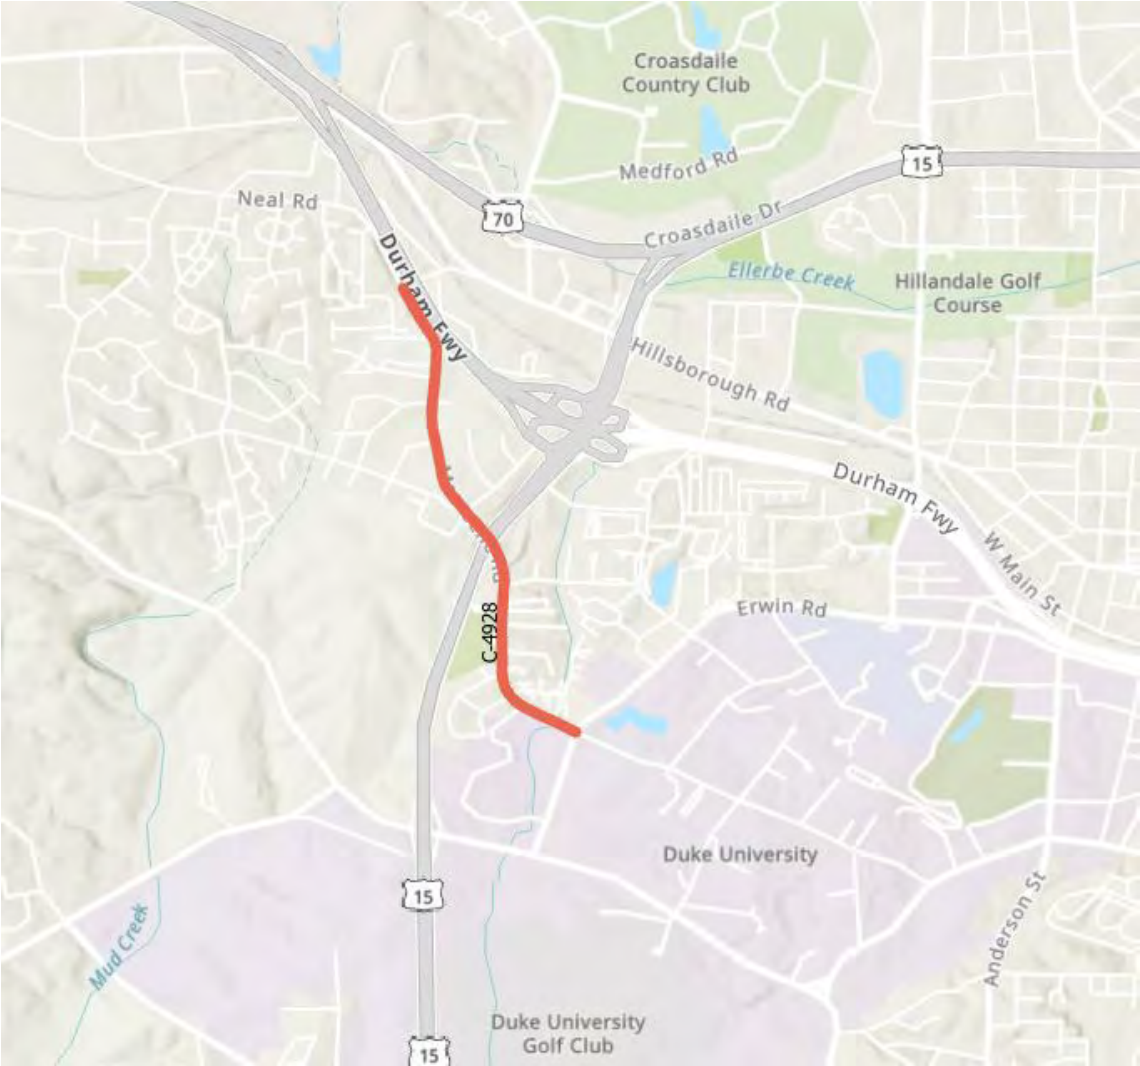






# U-4724 – Cornwallis Rd


|                                           |                                                                                                                                                  |
|-------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------|
| Description                               | Construct bike and pedestrian features along West Cornwallis Rd (SR 1158) from South Roxboro St (SR 2295) to Chapel Hill Rd (SR 1127) in Durham. |
| Project Manager                           | David Cates, Public Works                                                                                                                        |
| Funding                                   | Federal <del>\$6,364,610</del> \$6,450,853 (STBGDA)                                                                                              |
| Status                                    | Engineering                                                                                                                                      |
| Estimated Completion Date / Add'l Details | <del>1/1/2026</del> 9/1/2025                                                                                                                     |

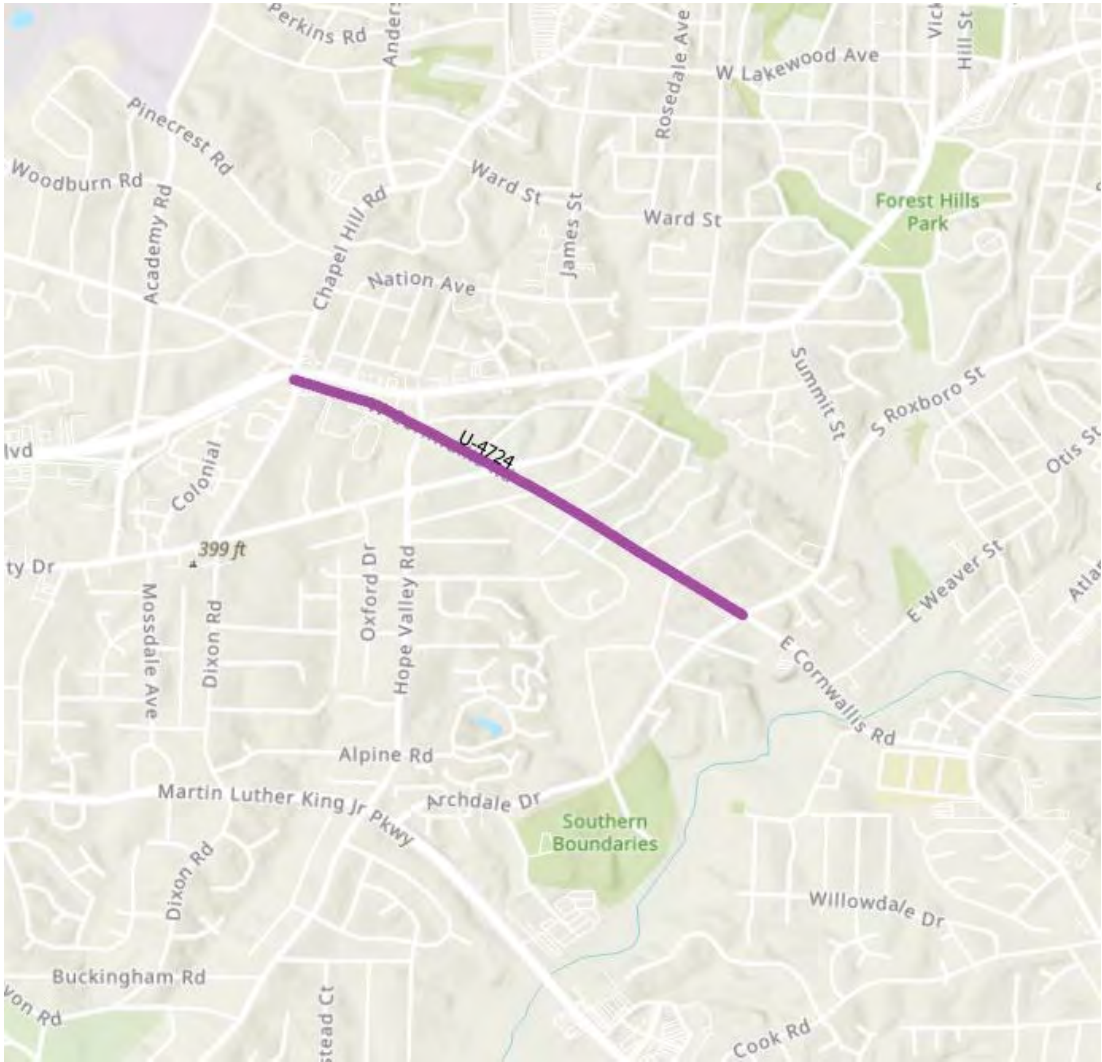



# U-4726HN – Hillandale Rd

|                                           |                                                                                     |
|-------------------------------------------|-------------------------------------------------------------------------------------|
| Description                               | Construct sidewalks and bicycle facilities along Hillandale Rd from I-85 to NC 147. |
| Project Manager                           | David Cates, Public Works                                                           |
| Funding                                   | Federal <del>\$3,857,642</del> \$3,859,257 (STBGDA, STP-DA)                         |
| Status                                    | Right Of Way                                                                        |
| Estimated Completion Date / Add'l Details | <del>8/1/2024</del> 11/1/2024                                                       |

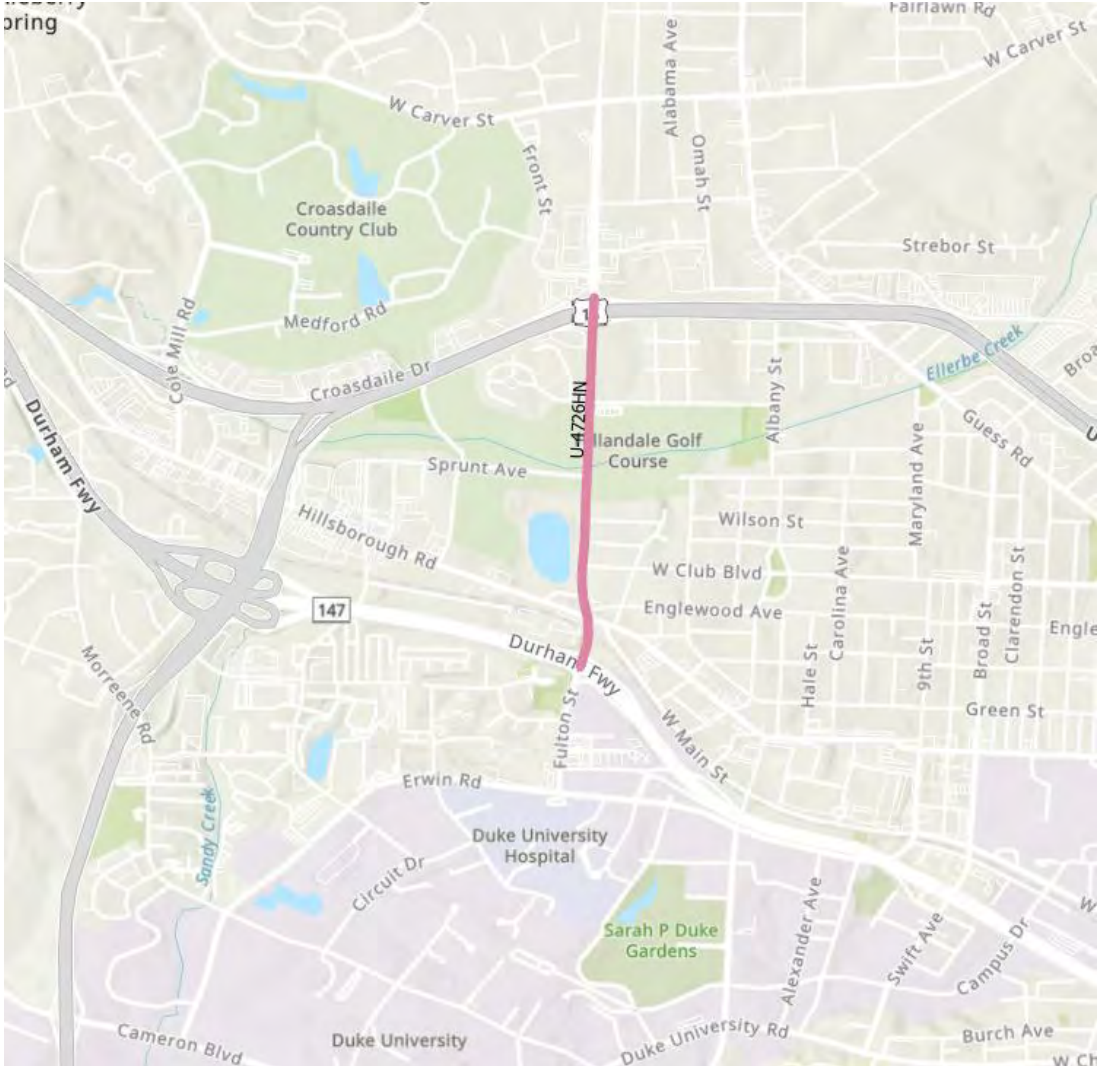






# U-4726HO – Carpenter-Fletcher Rd


|                                           |                                                                                                           |
|-------------------------------------------|-----------------------------------------------------------------------------------------------------------|
| Description                               | Construct sidewalks and bicycle facilities along Carpenter-Fletcher Rd from Woodcroft Pkwy to Alston Ave. |
| Project Manager                           | David Cates, Public Works                                                                                 |
| Funding                                   | Federal \$6,630,821 (STBGDA)                                                                              |
| Status                                    | Engineering                                                                                               |
| Estimated Completion Date / Add'l Details | 11/1/2025 2/1/2026                                                                                        |

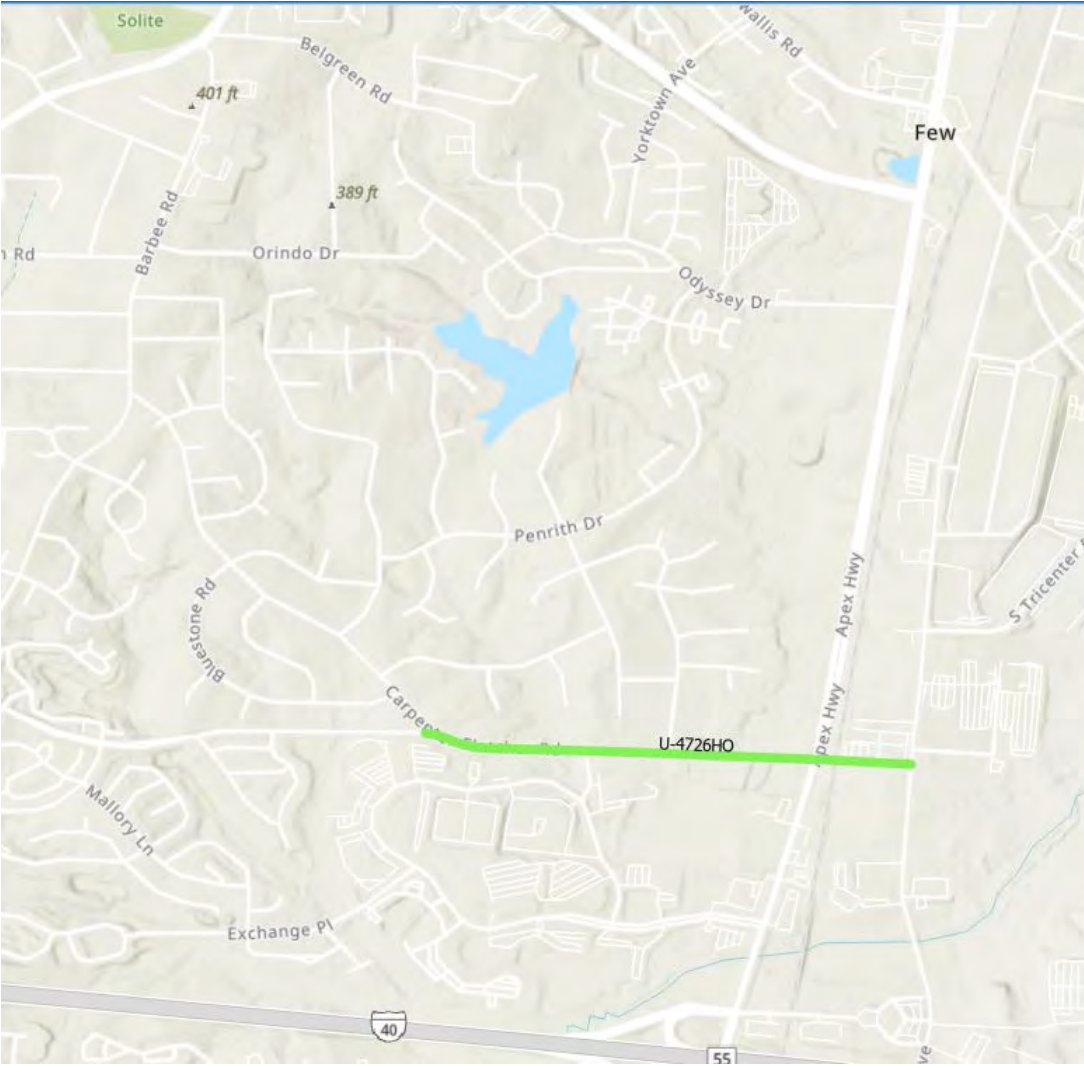



# EB-5720 – R. Kelly Bryant Bridge Trail

|                                           |                                                                                                        |
|-------------------------------------------|--------------------------------------------------------------------------------------------------------|
| Description                               | Construct a multi-use path from NC 55 to Drew-Granby Park, using the R. Kelly Bryant Bridge in Durham. |
| Project Manager                           | John Paces-Wiles, General Services                                                                     |
| Funding                                   | Federal \$4,182,800 \$6,502,800 (TAP, CPF)                                                             |
| Status                                    | Engineering                                                                                            |
| Estimated Completion Date / Add'l Details | 2025 6/1/2026                                                                                          |

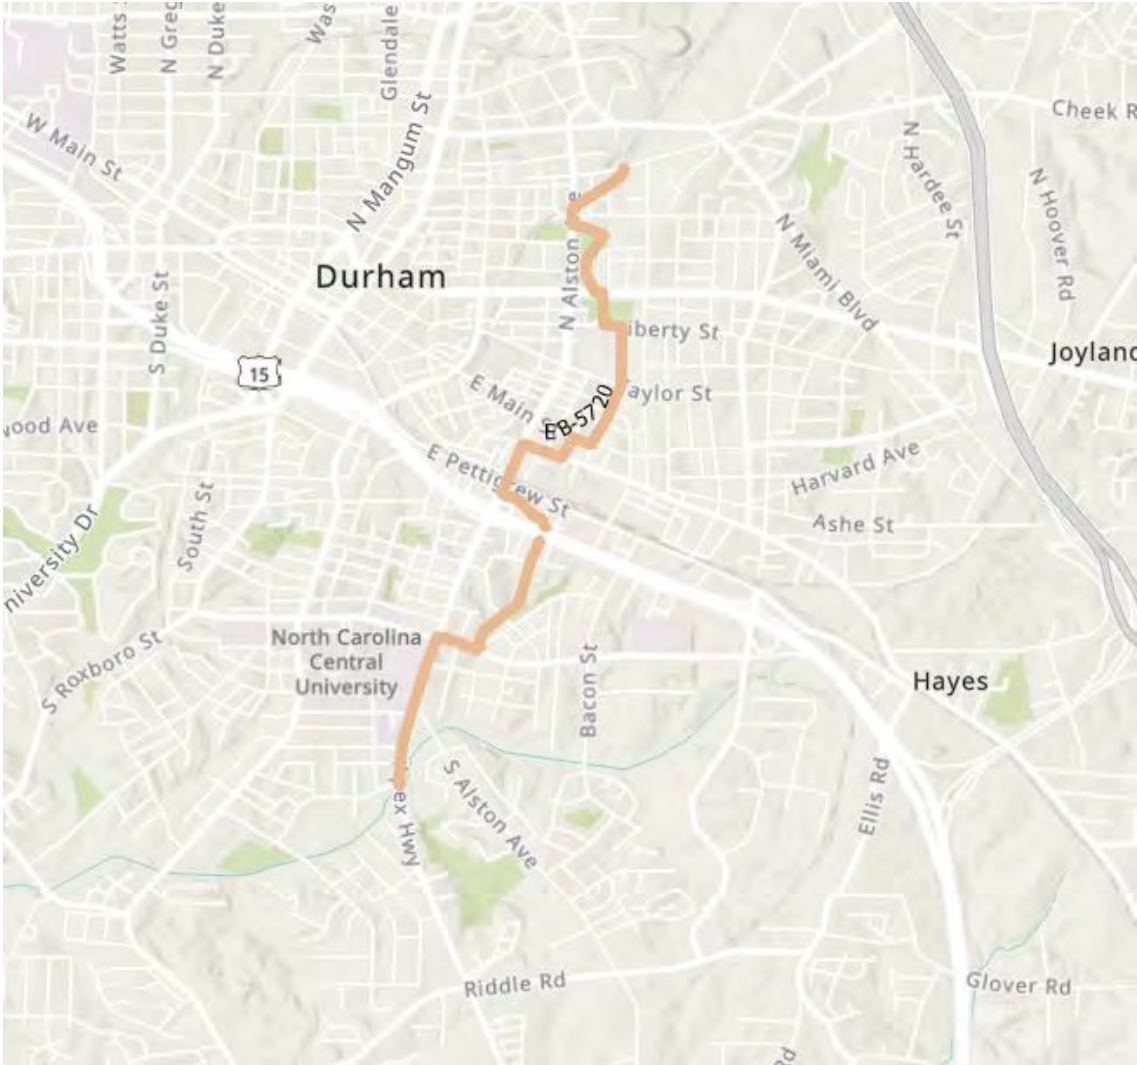






# EB-5904 – Durham Rail Trail


|                                           |                                                                                              |
|-------------------------------------------|----------------------------------------------------------------------------------------------|
| Description                               | Construct multiuse trail on former rail corridor in Durham from Pettigrew St to Avondale Dr. |
| Project Manager                           | Rod Florence, General Services                                                               |
| Funding                                   | Federal \$17,673,501 (STBGDA, TAP, RAISE)                                                    |
| Status                                    | Engineering                                                                                  |
| Estimated Completion Date / Add'l Details | 2025 11/1/2024                                                                               |

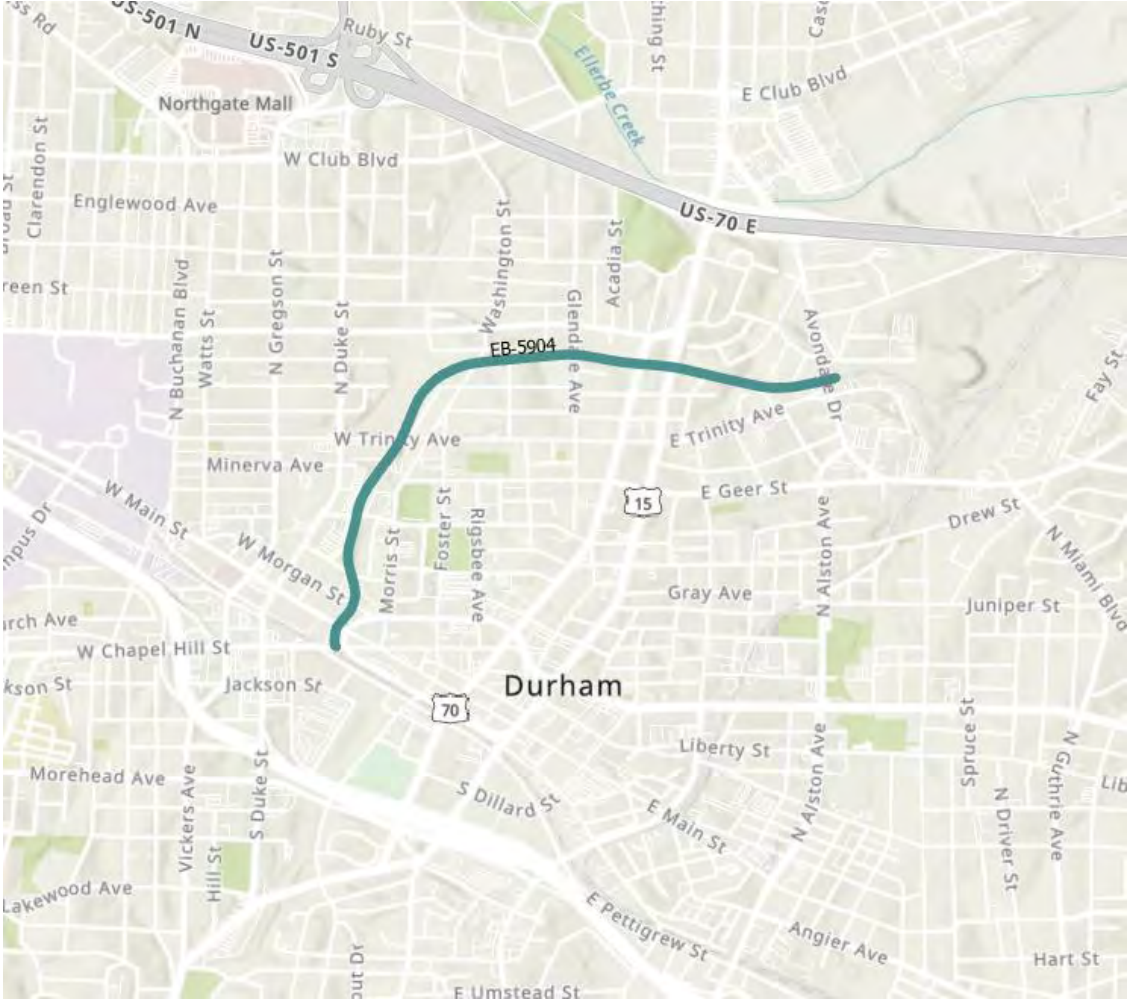



# EB-5837 – Third Fork Creek Trail Extension

|                                                  |                                                                                                                                            |
|--------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------|
| <b>Description</b>                               | Construct a shared use path and sidewalks in Durham from Southern Boundaries Park to the ATT. Install a beacon at SR 1158 (Cornwallis Rd). |
| <b>Project Manager</b>                           | John Paces-Wiles, General Services                                                                                                         |
| <b>Funding</b>                                   | Federal \$3,011,398 (TAP)                                                                                                                  |
| <b>Status</b>                                    | Engineering                                                                                                                                |
| <b>Estimated Completion Date / Add'l Details</b> | 2025                                                                                                                                       |

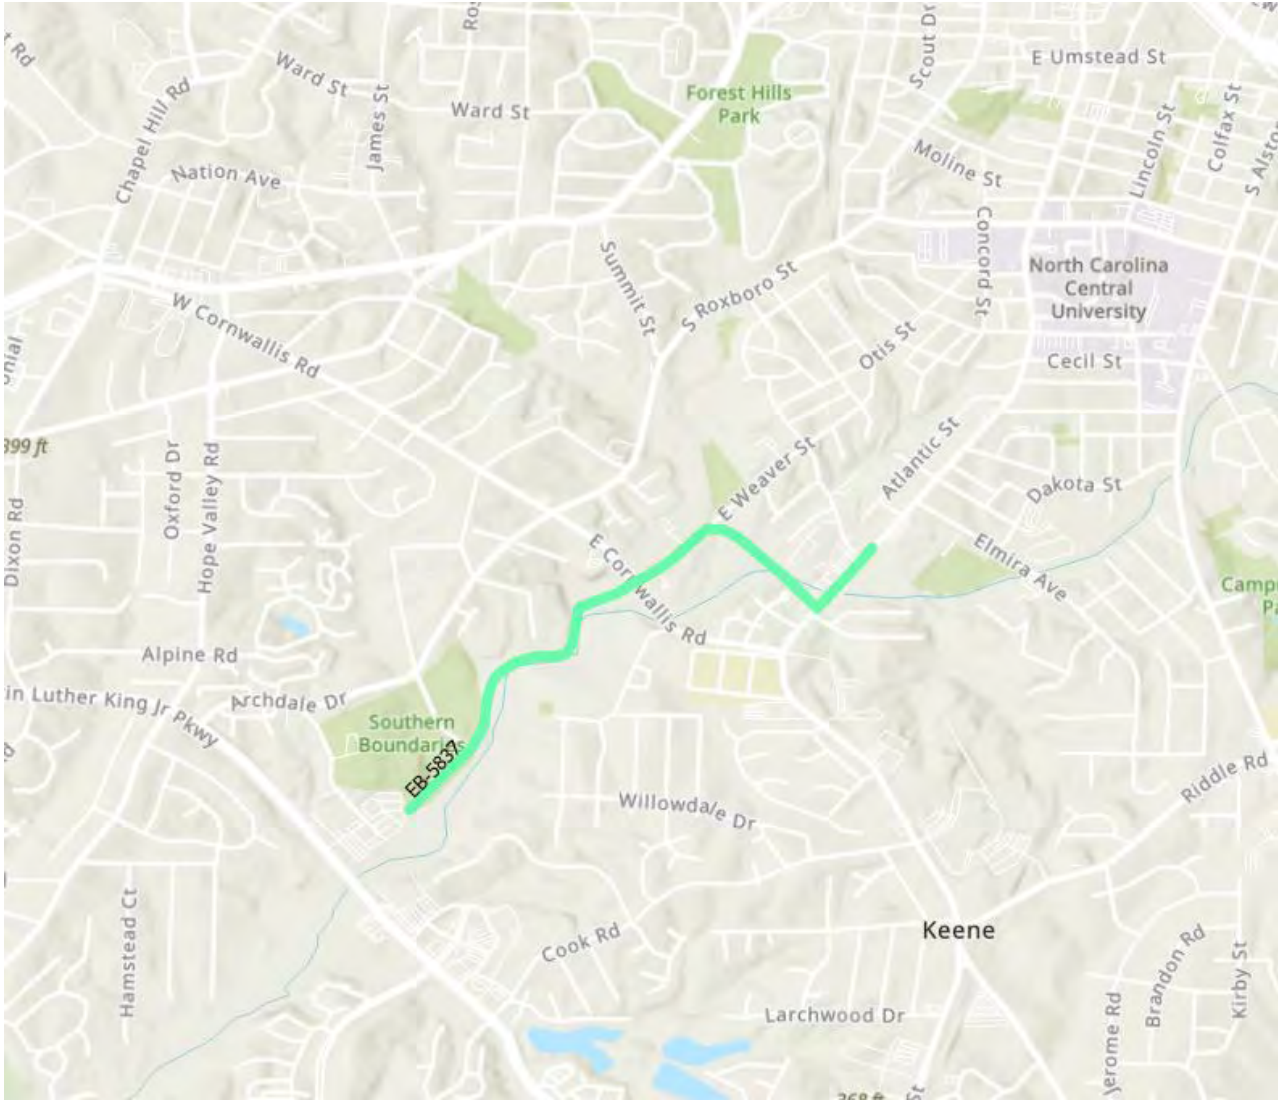







# C-5183B – Alston Ave

|                                           |                                                                 |
|-------------------------------------------|-----------------------------------------------------------------|
| Description                               | Construct sidewalk along Alston Ave from Capps St to Riddle Rd. |
| Project Manager                           | Ana Jaramillo, Public Works                                     |
| Funding                                   | Federal <del>\$565,000</del> \$1,077,577 (CMAQ)                 |
| Status                                    | Pre-Construction                                                |
| Estimated Completion Date / Add'l Details | <del>2024</del> 12/1/2023                                       |

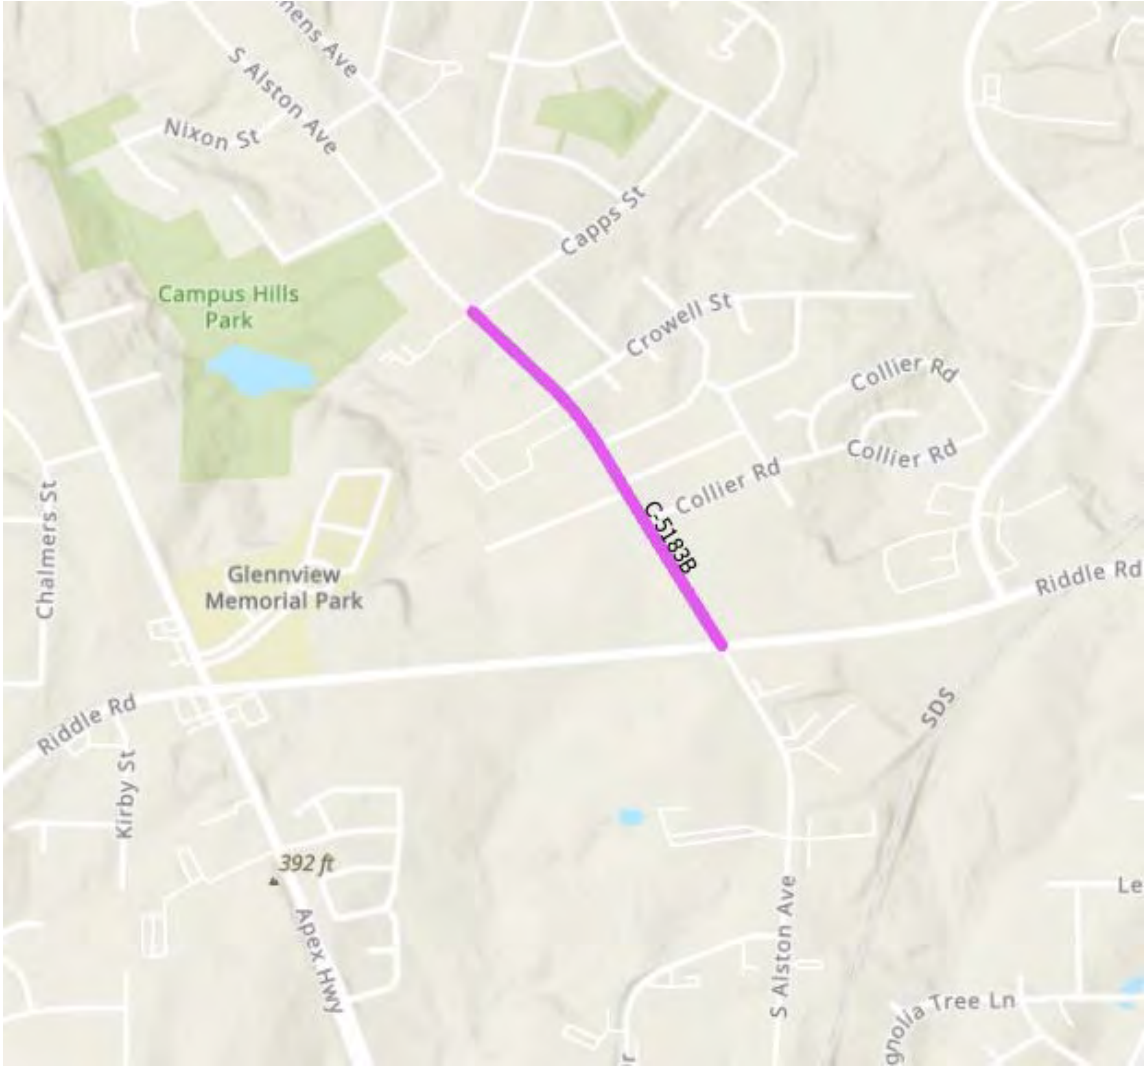



|                                           |                                                                                                                      |
|-------------------------------------------|----------------------------------------------------------------------------------------------------------------------|
| Description                               | Construct sections of sidewalk on south side of NC 54, from NC 55 to Research Triangle Park western limit in Durham. |
| Project Manager                           | David Cates, Public Works                                                                                            |
| Funding                                   | Federal \$716,000 (SRTS, TAP)                                                                                        |
| Status                                    | Right Of Way                                                                                                         |
| Estimated Completion Date / Add'l Details | <div>2/1/2024 9/1/2023</div>                                                                                         |

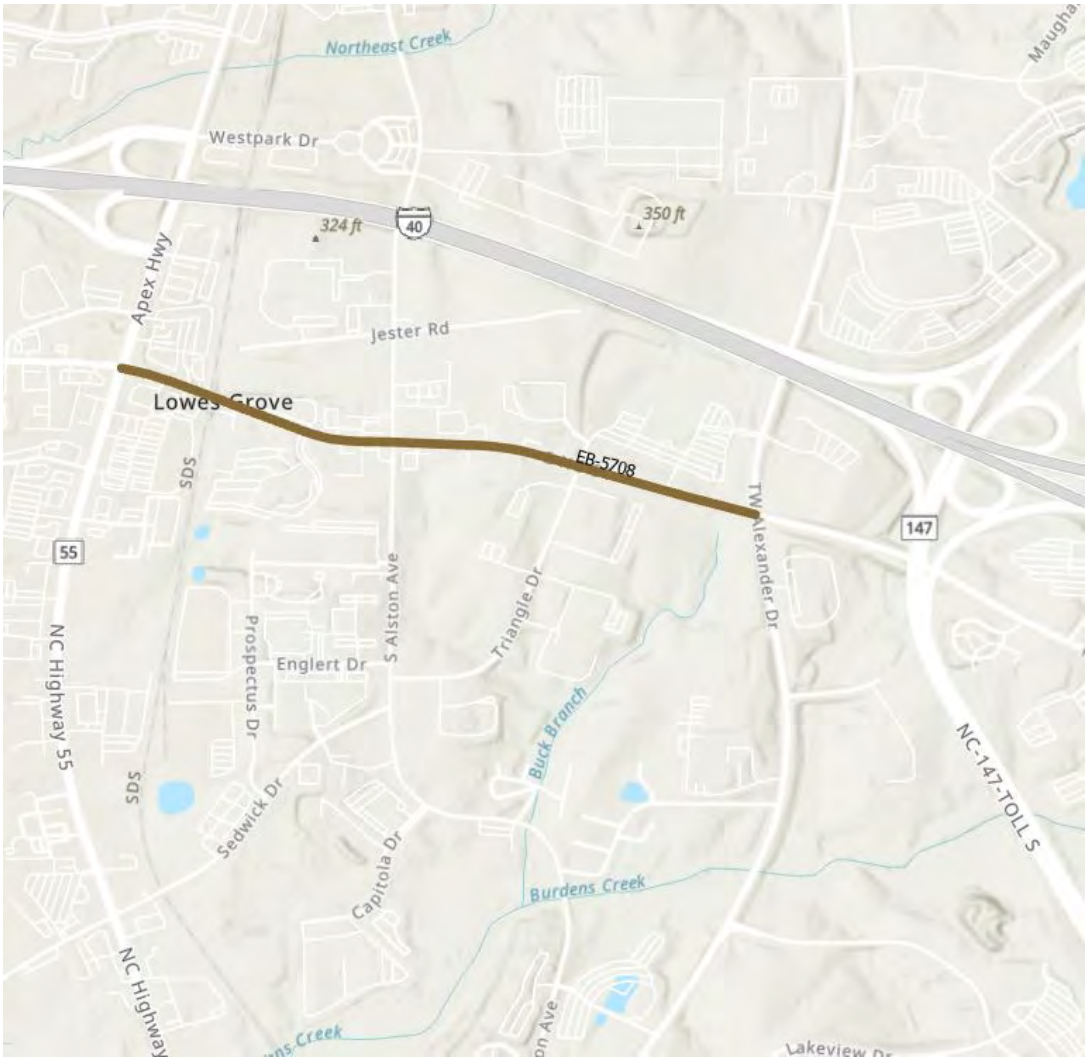






# EB-5704 – Raynor St


|                                           |                                                                                                          |
|-------------------------------------------|----------------------------------------------------------------------------------------------------------|
| Description                               | Construct sidewalk on one side of street along Raynor St from N Miami Blvd to North Hardee St in Durham. |
| Project Manager                           | David Cates, Public Works                                                                                |
| Funding                                   | Federal \$622,400 (TAP)                                                                                  |
| Status                                    | Right Of Way                                                                                             |
| Estimated Completion Date / Add'l Details | 5/1/2024                                                                                                 |

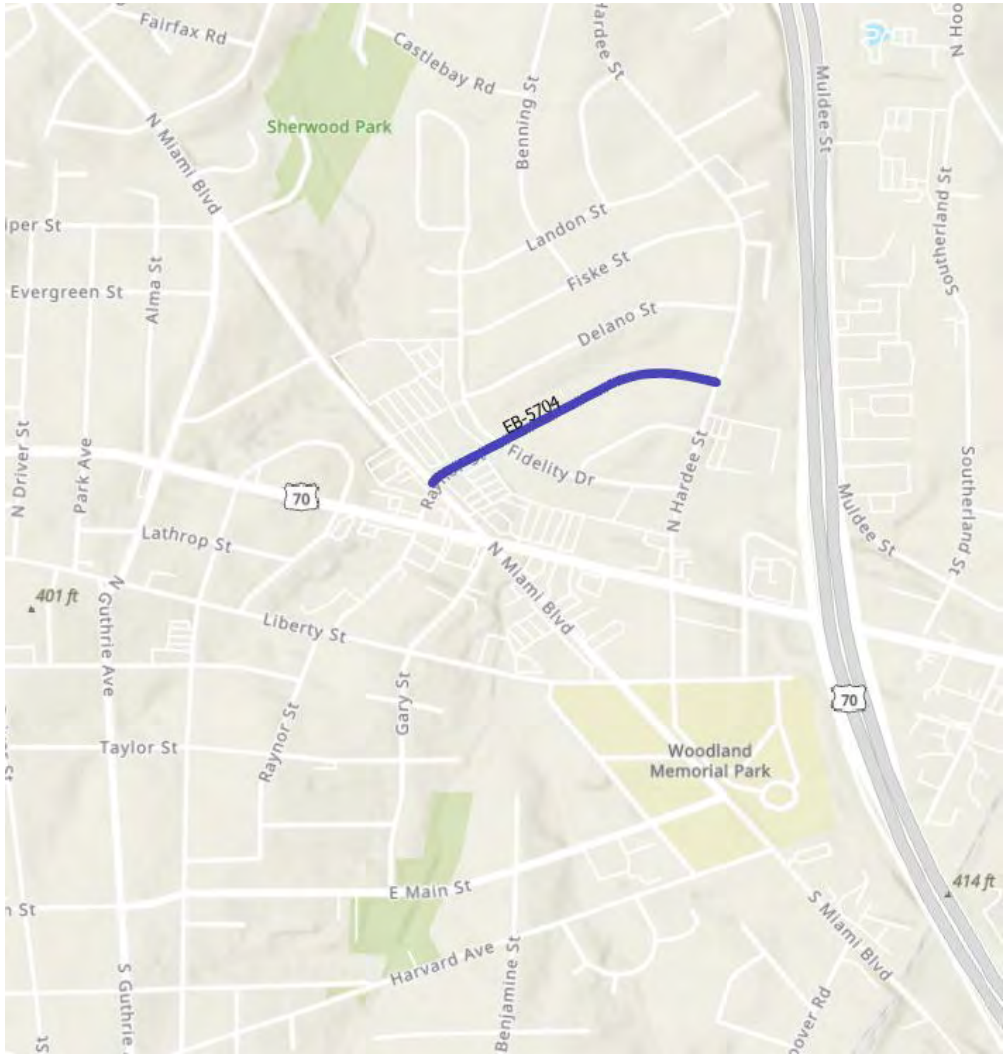



# EB-5703 – LaSalle St

|                                           |                                                                                                                                                              |
|-------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Description                               | Construct sidewalks on both sides of LaSalle St (Kangaroo Dr to US 70 BUS (Hillsborough Rd)), and on one side of LaSalle St (Hillsborough Rd to Sprunt Ave). |
| Project Manager                           | David Cates, Public Works                                                                                                                                    |
| Funding                                   | Federal \$1,564,000 (TAP)                                                                                                                                    |
| Status                                    | Right Of Way                                                                                                                                                 |
| Estimated Completion Date / Add'l Details | 11/1/2024                                                                                                                                                    |

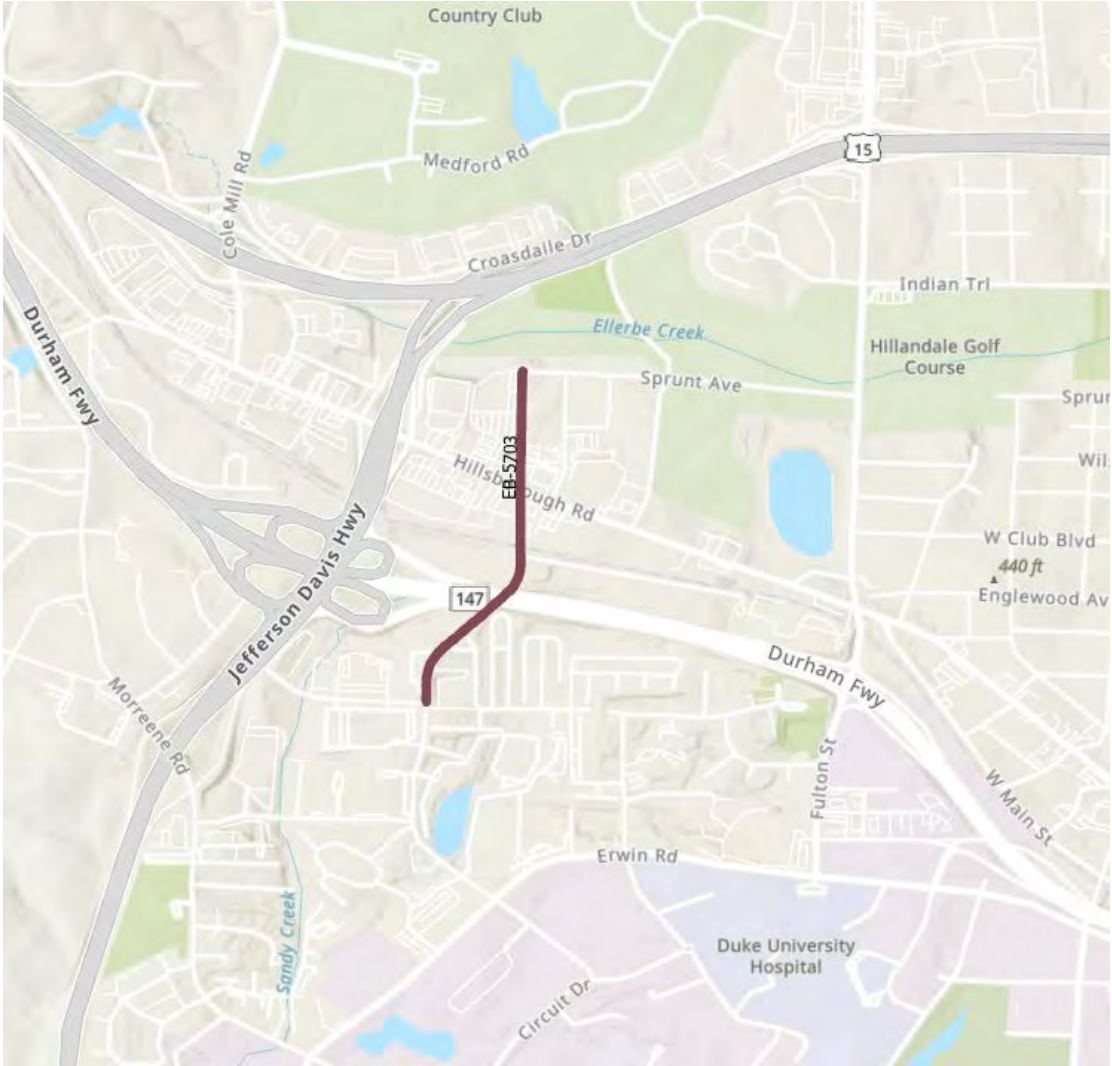






# EB-5715 – US 501 Bypass (N Duke St)


|                                           |                                                                                                                             |
|-------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------|
| Description                               | Construct sidewalk on east side of North Duke St from Murray Ave to US 501 BUS (North Roxboro Rd) to fill in existing gaps. |
| Project Manager                           | David Cates, Public Works                                                                                                   |
| Funding                                   | Federal \$3,819,403 (TAP)                                                                                                   |
| Status                                    | Right Of Way                                                                                                                |
| Estimated Completion Date / Add'l Details | 8/1/2025                                                                                                                    |

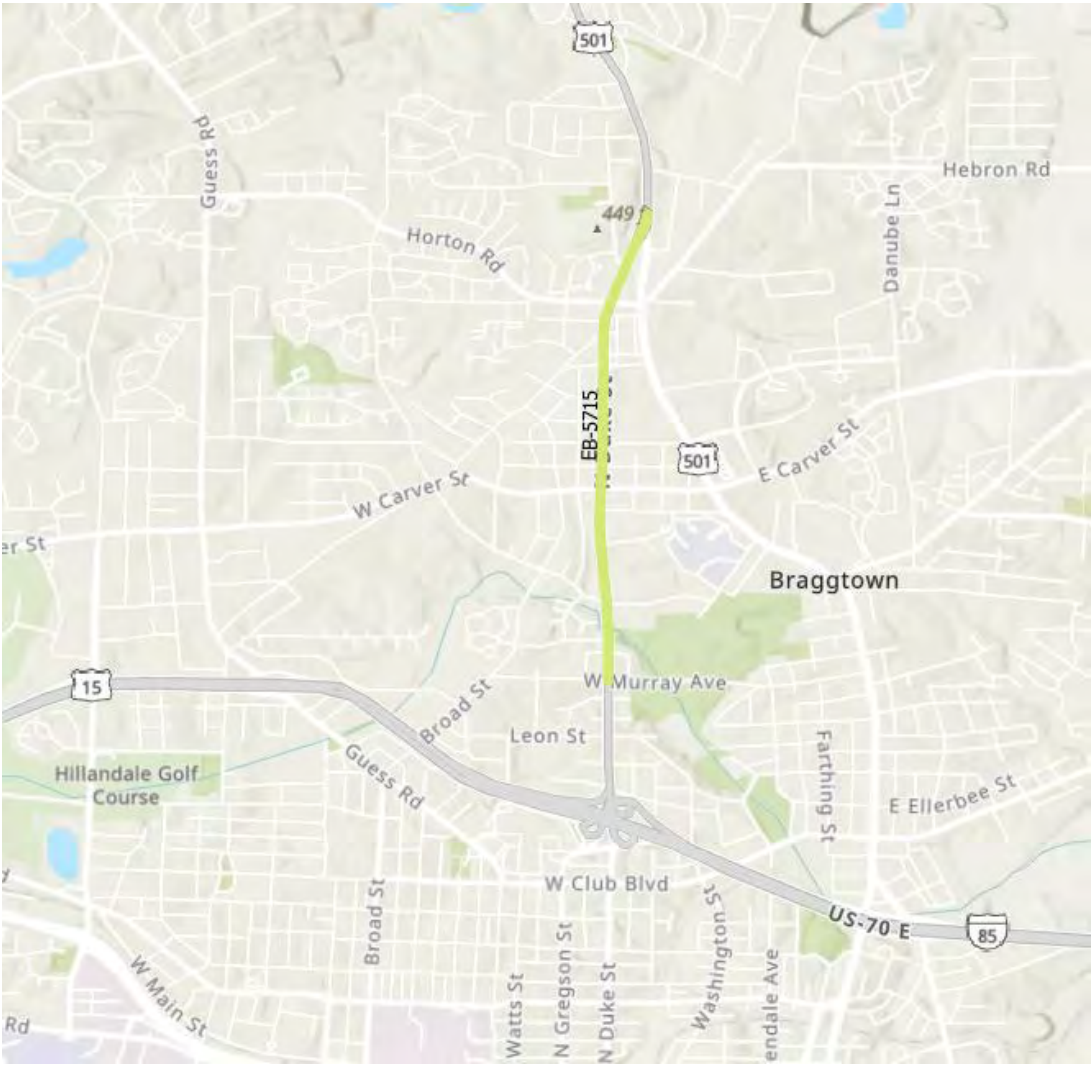



# EB-5835 – NC 55 Sidewalk

|                                           |                                                                                                                |
|-------------------------------------------|----------------------------------------------------------------------------------------------------------------|
| Description                               | Construct sidewalk on east side of NC 55 from SR 1171 (Riddle Rd) to Cecil St in Durham. Fill in missing gaps. |
| Project Manager                           | Erin Convery, Transportation                                                                                   |
| Funding                                   | Federal \$1,215,014 (STBGDA, TAP)                                                                              |
| Status                                    | Project Set Up                                                                                                 |
| Estimated Completion Date / Add'l Details | 2026                                                                                                           |

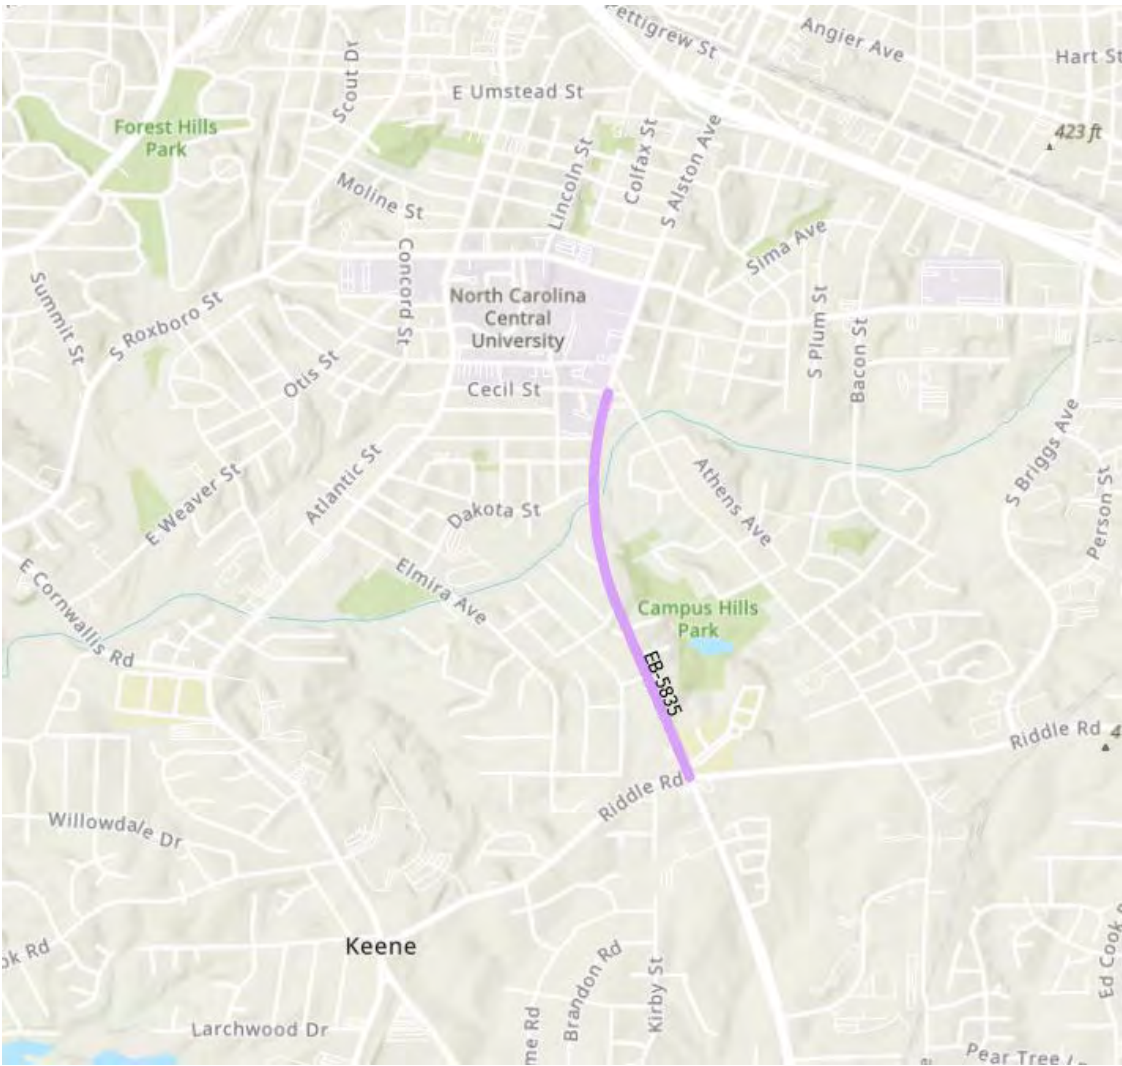






# EB-5834 – NC 157 (Guess Rd)

|                                           |                                                                                                                 |
|-------------------------------------------|-----------------------------------------------------------------------------------------------------------------|
| Description                               | Construct sidewalks on both sides of NC 157 (Guess Rd) from SR 1407 (West Carver St) to Hillcrest Dr in Durham. |
| Project Manager                           | Erin Convery, Transportation                                                                                    |
| Funding                                   | Federal \$1,431,906 (STBGDA, TAP)                                                                               |
| Status                                    | Project Set Up                                                                                                  |
| Estimated Completion Date / Add'l Details | 2026                                                                                                            |

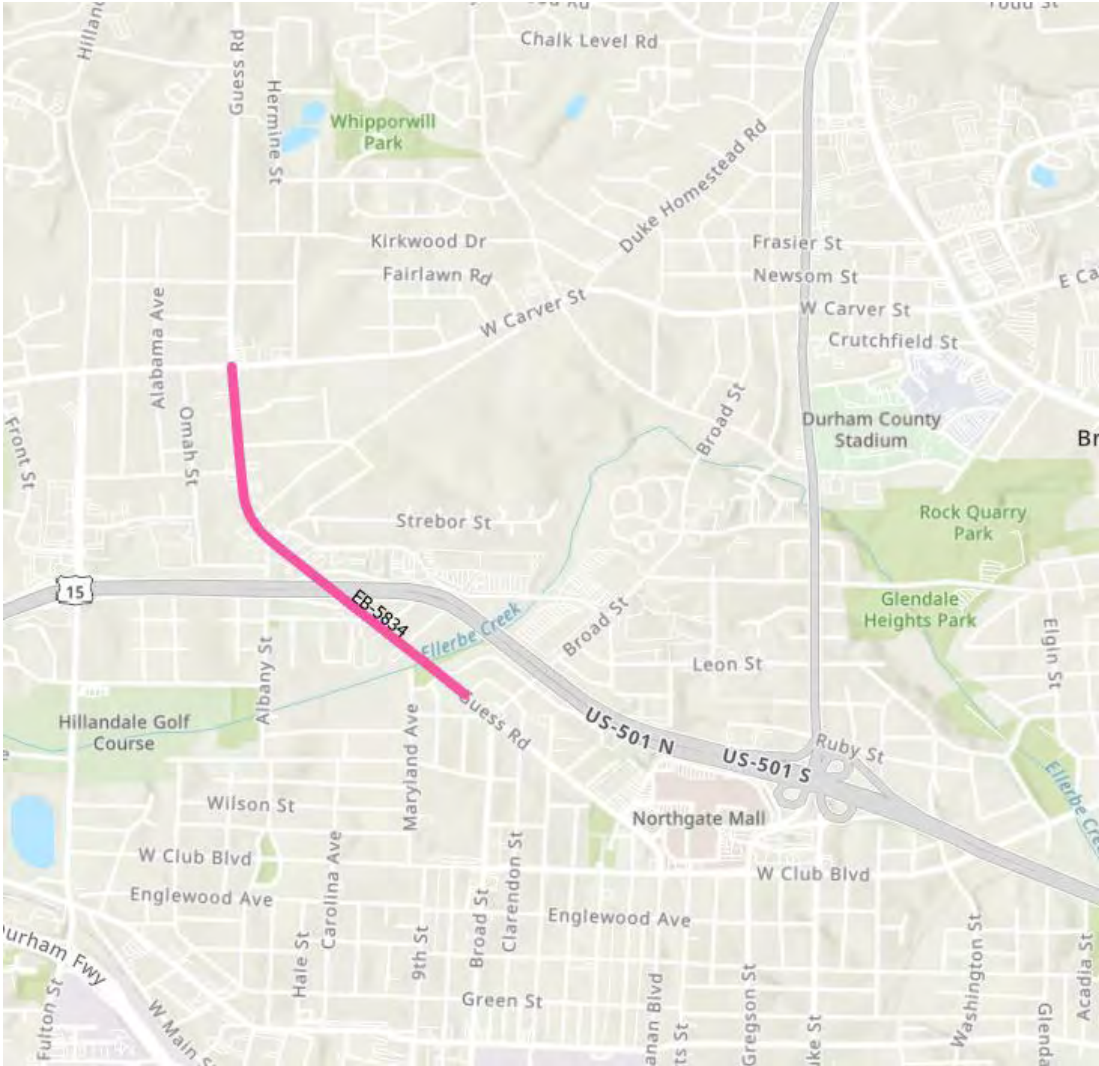

# C-5605H – Downtown Durham Wayfinding Program

|                                           |                                                                                                 |
|-------------------------------------------|-------------------------------------------------------------------------------------------------|
| Description                               | Install signage and kiosks throughout Downtown Durham to facilitate navigation and parking.     |
| Project Manager                           | Shauna Parker <del>Todd Tingler, General Services</del> <del>Eric Simpson, Transportation</del> |
| Funding                                   | Federal \$601,913 (CMAQ)                                                                        |
| Status                                    | Construction <i>Pre-Construction</i>                                                            |
| Estimated Completion Date / Add'l Details | <i>2023 2028</i>                                                                                |

